




FEDERAL MINISTRY OF WORKS & HOUSING

REPORT OF MONITORING & EVALUATION TEAM ON CAPITAL & CONSTITUENCY PROJECTS AWARDED IN 2019




REPORT ON MONITORING & EVALUATION

**CONDUCTED IN DECEMBER, 2020
ANCHORED BY PLANNING, RESEARCH
AND STATISTICS DEPARTMENT**

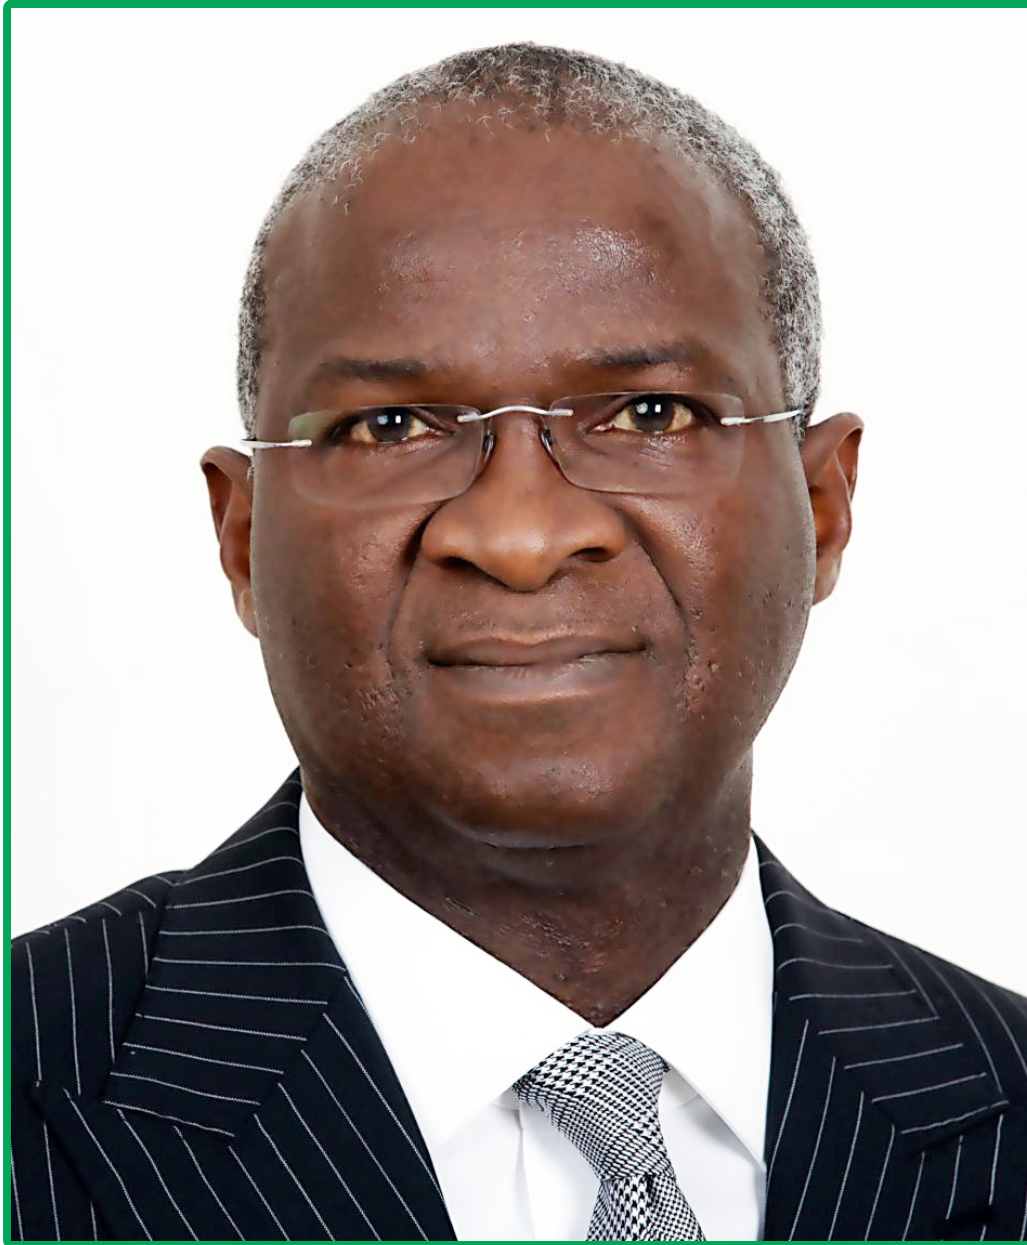

HIS EXCELLENCY
BABATUNDE RAJI FASHOLA (SAN)
HONOURABLE MINISTER
FEDERAL MINISTRY OF WORKS & HOUSING

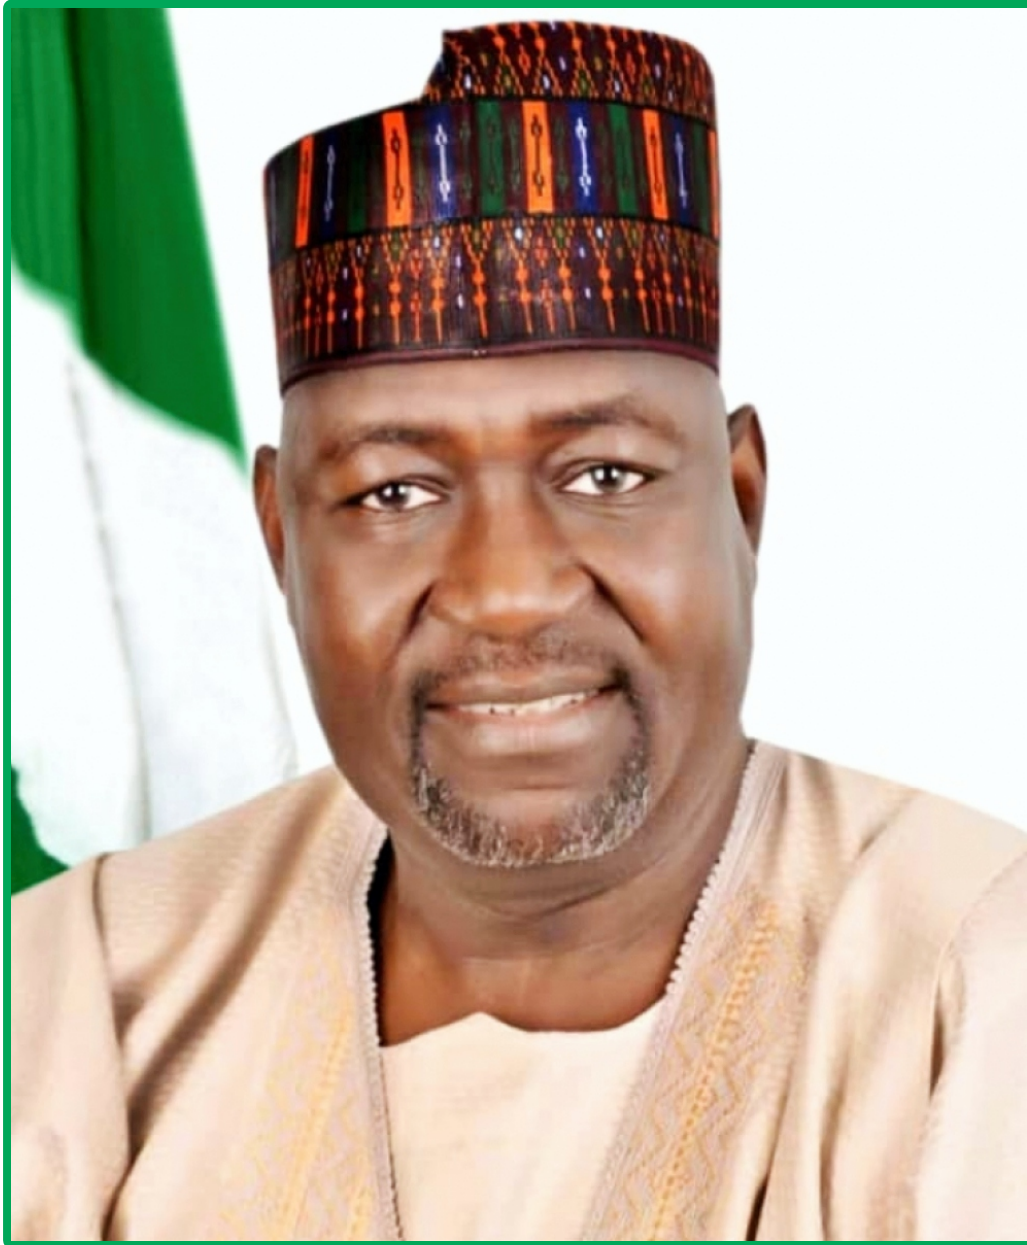

ENGR. ABUBAKAR ALIYU (FNSE)
HONOURABLE MINISTER OF STATE
FEDERAL MINISTRY OF WORKS & HOUSING



BABANGIDA HUSSAINI
PERMANENT SECRETARY
FEDERAL MINISTRY OF WORKS & HOUSING

TABLE OF CONTENTS

Preamble:-----	x
Methodology:-----	x
Findings:-----	xi
Observation-----	xi
Challenges-----	xiii
Recommendations-----	xiv
List of Officers and Zones-----	xv

LOCATIONS OF PROJECTS IN STATES AND LGAs

NORTH CENTRAL:-----	1
1.0 FCT:-----	1
1.0 AMAC:-----	1
1.01 AMAC:-----	2
1.02 AMAC-----	3
1.03 AMAC-----	4
1.04 AMAC-----	5
2.0 NIGER STATE:-----	6
2.0 BARIKIN SALE:-----	6
2.01 BIDA LGA:-----	7
2.02 MINNA:-----	8
2.03 WUSHI LGA:-----	9
2.04 KONTAGORA LGA:-----	10
2.05 KONTAGORA LGA:-----	11
2.06 BIDA LGA:-----	12
3.0 KOGI STATE:-----	13
3.0 LOKOJA:-----	13
3.01 KOTON-KARFE:-----	14
3.02 KOTON-KARFE:-----	15
3.03 KOTON-KARFE:-----	16
3.04 ADAVI:-----	17
3.05 DEKINA:-----	18
3.06 IMANI:-----	19
3.07 OKENE:-----	20
3.08 OYENYI:-----	21
4.0 NASARAWA STATE:-----	22
4.0 LAFIA:-----	22
4.01 LAFIA:-----	23
4.02 KOKONA, KEFFI AND KARU:-----	24
4.03 KARU:-----	25
5.0 PLATEAU STATE:-----	26
5.0 BOKKOS:-----	26
5.01 PANKSHIN:-----	27
5.02 KANKE:-----	28
5.03 PANKSHIN:-----	29
5.04 BOKKOS L.G.A, MANGUS L.G.A :-----	30
6.0 BENUE STATE:-----	31
6.0 GBBOKO:-----	31
6.01 MAKURDI:-----	32
6.02 MAKURDI:-----	33

6.03	MAKURDI:-----	34
6.04	APA LGA, GWER- EAST LGA, GWER- WEST LGA:-----	35
6.05	KONSHISHA LGA:-----	36
7.0	KWARA STATE:-----	37
7.0	EDU:-----	37
7.01	OWU ISIN:-----	38
7.02	ILORIN SOUTH:-----	39
7.03	ILORIN SOUTH:-----	40
7.04	OYUN:-----	41
7.05	PATEGI:-----	42
7.06	PATEGI:-----	43
	NORTH EAST:-----	44
8.0	ADAMAWA STATE:-----	44
8.0	YOLA SOUTH:-----	44
8.01	YOLA SOUTH:-----	45
8.02	DEMSA LGA :-----	46
9.0	BAUCHI STATE:-----	47
9.0	TAFAWA BALEWA L.G.A:-----	47
9.01	TAFAWA BALEWA L.G.A:-----	48
9.02	TAFAWA BALEWA L.G.A:-----	49
9.03	TAFAWA BALEWA L.G.A:-----	50
9.04	TAFAWA BALEWA L.G.A:-----	51
10.0	BORNO STATE:-----	52
10.0	MAIDUGURI:-----	52
10.01	MAIDUGURI:-----	53
10.02	MAIDUGURI:-----	54
10.03	MAIDUGURI:-----	55
11.0	YOBE STATE:-----	56
11.0	JAKUSKO:-----	56
11.01	POTISKUM:-----	57
11.02	POTISKUM:-----	58
11.03	POTISKUM:-----	59
11.04	BADE WEST:-----	60
11.05	KARASUWA:-----	61
12.0	GOMBE STATE:-----	62
12.0	BALLANGA:-----	62
12.01	AKKO:-----	63
12.02	GOMBE:-----	64
12.03	GOMBE:-----	65
12.04	AKKO:-----	66
	NORTH WEST:-----	67
13.0	KANO STATE:-----	67
13.0	GAWUNA:-----	67
13.01	NASARAWA LGA:-----	68
13.02	NASARAWA LGA:-----	69
13.03	KUMBOTSO LGA:-----	70
13.04	TSANYAWA LGA:-----	71
13.05	NASARAWA:-----	72
13.06	NASARAWA:-----	73
14.0	KADUNA STATE:-----	74
14.0	ZARIA LGA KADUNA STATE:-----	74

14.01	ZARIA LGA, KADUNA:-----	75
14.02	ZARIA LGA, KADUNA:-----	76
14.03	ZARIA LGA, KADUNA:-----	77
14.04	ZARIA LGA, KADUNA:-----	78
14.05	KADUNA NORTH, KADUNA :-----	79
15.0	KATSINA STATE:-----	80
15.0	KANKIA:-----	80
15.01	KANKARA:-----	81
15.02	MALUMFASHI:-----	82
15.03	KANKARA:-----	83
15.04	KUSADA:-----	84
15.05	DAUIA:-----	85
15.6	KUSADA:-----	86
16.0	JIGAWA STATE:-----	87
16.0	TAURA:-----	88
16.01	KAFIN HAUSA LGA:-----	88
16.02	DAGANA GURI LGA:-----	89
16.03	BALLAMI KAZAURE LGA:-----	90
16.04	KAZAURE LGA:-----	91
16.05	YANKWASHI LGA:-----	92
16.06	YANKWASHI LGA:-----	93
16.07	BABURA LGA:-----	94
16.08	BIRINIWA LGA:-----	95
16.09	BIRINIWA LGA:-----	96
16.10	BIRINIWA LGA:-----	97
17.0	SOKOTO STATE:-----	98
17.0	SOKOTO:-----	98
17.01	SOKOTO:-----	99
18.0	KEBBI STATE:-----	100
18.0	BAGUDO:-----	100
18.01	JEGA:-----	101
18.02	BIRNIN KEBBI:-----	102
18.03	JEGA:-----	103
18.04	BAGUDO:-----	104
18.05	KALGO, ALIERO:-----	105
18.06	ARGUNGU, AUGIE:-----	106
19.0	ZAMFARA STATE:-----	107
19.0	GUSAU:-----	107
	SOUTH EAST:-----	108
20.0	IMO STATE:-----	108
20.0	IHALA ORLU:-----	108
20.01	ISIALA MBANO L.G.A:-----	109
20.02	IBEME ISIALA MBANO L.G.A:-----	110
20.03	IBEME ISIALA MBANO L.G.A:-----	111
20.04	EHIME MBANO L.G.A.:-----	112
20.05	EHIME MBANO L.G.A.:-----	113
20.06	UMUEZIE NGURU, AGOHIMO MBAISE:-----	114
20.07	EHIME MBANO L.G.A.:-----	115
21.0	ENUGU STATE:-----	116
21.0	ENUGU SOUTH:-----	116
21.01	AWGU:-----	117

22.0 EBONYI STATE:	118
22.0 EKKA COMMUNITY EZZA NORTH LGA:	118
22.01 EKKA COMMUNITY NORTH EBONYI:	119
22.02 EZI-AKANI UKPA COMMUNITY, AFIKPO:	120
22.03 AMAIZU VILLAGE, AFIKKPO:	121
22.04 IBAGWO-EKKA COMMUNITY, AFIKPO:	122
23.0 ABIA STATE:	123
23.0 BENDE, ISIKWUATOR & OHAOFIA:	123
23.01 OZARTA VILLAGE, UKWA WEST LGA:	124
23.02 CENTRAL PRIMARY SCHOOL, OBIOHIA:	125
23.03 UMUAHIA SOUTH LGA:	126
23.04 OHUHU-UMUAHIA NORTH LGA:	127
23.05 BENDE LGA:	128
23.06 OLOKORO SOUTH LGA:	129
SOUTH WEST:	130
24.0 OYO STATE:	130
24.0 IBADAN:	130
24.01 IBADAN:	131
24.02 AFIJIO:	132
24.03 OGOBOMOSHO:	133
24.04 OYO:	134
24.05 ALAGBON:	135
25.0 OGUN STATE:	136
25.0 OTA:	136
25.01 OTA:	137
25.02 OTA:	138
25.03 OTA:	139
25.04 IPOKIA:	140
25.05 IJEBU-ODE:	141
26.0 OSUN STATE:	142
26.0 OSOGBO:	142
26.01 OSOGBO:	143
26.02 EDE:	144
27.0 LAGOS STATE:	145
27.0 ETI-OSA:	145
27.01 (BARIGA):	146
27.02 SURULERE:	147
27.03 IKORODU:	148
27.04 IKORODU:	149
27.05 SURU LERE:	150
27.06 SURU LERE:	151
27.07 SURU LERE:	152
27.08 AGUNTASHOLO PRIMARY SCHOOL:	153
27.09 ODOLOWU PRIMARY SCHOOL:	154
28.0 EKITI STATE:	155
28.0 EKITI SOUTH WEST:	155
28.01 ADO EKITI:	156
28.02 EYIO EKITI:	157
28.03 EYIO EKITI:	158
28.04 EYIO EKITI:	159
28.05 EYIO EKITI:	160

29.0 ONDO:	161
29.0 AKURE NORTH:	161
29.01 AKURE NORTH:	162
29.02 OKITIPUPA:	163
SOUTH SOUTH:	164
30.0 RIVERS:	164
30.0 AHOADA EAST:	164
30.01 PORTHARCOURT CITY:	165
30.02 PORTHARCOURT CITY:	166
30.03 PORTHARCOURT CITY:	167
30.04 PORTHARCOURT CITY:	168
31.0 EDO STATE:	169
31.0 ETSAKO WEST LGA:	169
31.01 ETSAKO WEST LGA:	170
31.02 AKOKO EDO LGA:	171
31.03 ETSAKO CENTRAL LGA:	172
31.04 ETSAKO WEST LGA:	173
32.0 BAYELSA STATE:	174
32.0 YENEGOA:	174
33.0 CROSS RIVER:	175
33.0 OGOJA LGA:	175
33.01 OBUDU LGA:	176
33.02 YALA LGA:	177
33.03 OBALIKU/OBUDU/BEKWARRA LGA:	178
33.04 OGOJA LGA:	179
34.0 DELTA STATE:	180
34.0 OSHIMILI NORTH:	180
34.01 ANIOCHA NORTH:	181
34.02 IKA SOUTH LGA:	182
34.03 ISOKO NORTH:	183
34.04 ISOKO NORTH:	184
35.0 AKWA IBOM:	185
35.0 IBESEKPO ASUTAW:	185
35.01 IBESEKPO ASUTAN:	186
35.02 IBESIKPO ASUTAN:	187

PREAMBLE

Following the approval of the Permanent Secretary Mr Ernest Umakhihe on the conduct of 2020 Monitoring/Verification exercise on Capital and Constituency Projects nationwide, a Joint Monitoring Team was set up under the Coordination of Mr O.B Martins, Director Planning, Research and Statistics.

2. In view of this, a circular was sent to Project Implementing Departments to forward lists of Capital and Constituency Projects awarded in 2019. As a result of the large number of the Projects, (8) days was approved by the Permanent Secretary to carry out the exercise. This was to enable the Team to locate and verify and Verification exercise was grouped in two (2) phases so as to cover the six (6) Geo-political zones of the Federation. The exercise was scheduled to commence from 5th October 12th October, 2020 for Group 1 Comprises of North West, North Central and South West Geo Political zones While the Group 2 which comprises of South East, South South and North East Geo-political zone was to commence from 19th October to 26th October, 2020. The end result of this exercise will help the Ministry to have a full data of Projects awarded, executed and proper Budget Implementation plan.

3. A brief meeting was Organized by the Department of Planning, Research and Statistics of the Ministry in preparation for the Monitoring exercise. Nominated officers from various department were in attendance. The meeting emphasized the essence of the exercise and the use of Monitoring Templates and other documents that must be authenticated by the field Controllers or their representatives.

METHODOLOGY:

The following strategies were adopted for the assignments:

1. A circulars were sent to relevant departments to nominate two (2) officers for the assignment
2. A meeting was held with the nominated officers on how to carry out the Monitoring and varification exercise.
3. One (1) officer was assigned to cover Projects in each of the 36 States of the Federation and FCT.
4. Letters of Introduction were given to each officers which specifies the purpose of the assignment and introduction to the Field office Controllers.
5. A WhatsApp platform was created to monitor members of the Monitoring Team to ensure proper follow –up.
6. Time stamp application was down loaded by Team members on their Phones to show date and time Photographs were taking at the Project sites.

FINDINGS:

8. A total of 200 projects were listed for physical verification during the exercise. These include projects for the Special Project Unit (163), Engineering services (31) Federal Government Secretariat in the State(6)
9. Out of these, 162 projects were fully completed. 9 were On-going while 1 was abandoned. However, 28 projects sites in Kaduna, Enugu, Niger, Bayelsa, Anambra, Nassarawa and Edo States could not be visited due to security problems and inability to locate some project sites. Arising from the physical verification to the various projects sites are the detailed reports given on the projects and summary of the verification exercise tabulated hereunder.

OBSERVATIONS

The team was scheduled to visit 199 projects however 172 projects were physically verified. The breakdown of physically verified project in each of the Zone is as follows.

NORTH-WEST GEO-POLITICAL ZONE: In this zone, 38 projects were listed for verification, but 36 were verified. Out of these verified projects 36 projects were fully completed.

NORTH-EAST GEO-POLITICAL ZONE: Out of 35 Projects that were listed, 28 were verified, 28 of the verified projects were fully completed.

NORTH-CENTRAL GEO-POLITICAL ZONE: There were 42 projects listed for verification in this zone. However, 39 projects were verified, out of which 37 projects were fully completed, 1 was on-going while the remaining 1 was abandoned.

(a) The On-Going Projects : Projects that is on – going in the Zone include:

- i. The Construction of Completion of Construction of Federal Secretariat Lafia, Nasarawa State awarded to M/S Faplin Nig. Ltd.

(b) Abandoned Project: The abandoned project in the zone include:

- i Rehabilitation of Maintenance of fire fighting system Federal Secretariat Jos Plateau State awarded to M/S Daserz Construction Ltd.

SOUTH- EAST GEO-POLITICAL ZONE: There were 29 projects listed for verification in the zone. Out of which 18 projects were verified. However 16 of the projects were fully completed, 2 projects were on-going.

(a) The on-going projects include:

- (i) Construction of Motorized Borehole at Ehime Mbanjo awarded to M/S Defensive & Protective Concepts Ltd.
- (ii) Construction of Roads, Drains and Bridge at Ihiala Orlu, Umuduru Express Way Spur to Ohiara Bridge, Ihtenasa Orsu, Imo State.

SOUTH-WEST GEO-POLITICAL ZONE: A total of 31 projects were listed for verification in the zone. 30 projects were verified. Out of these verified projects, 27 were fully completed. and 3 were on-going projects. The on- going projects include:

- (i) Construction of Block of Classrooms at Erin Osho Itire, Aiyetoro Aguda, Jiandu Aguda, Sanya Grammer School, Odolowo Primary School, Ijeshatedo, LA Primary School, Orile and Akanji Primary School Ikate, Lagos State awarded to Faith Universal Nig. Ltd.
- (ii) Completion of Construction & Furnishing of Federal Secretariat at Ekiti State awarded to M/S Deux Projects Ltd. and
- (iii) Completion of Construction of federal Secretariat Osun State awarded to M/S Golden Construction Ltd.

SOUTH-SOUTH GEO-POLITICAL ZONE: In this zone, 24 projects were listed for verification, out of which, 21 were verified. 18 of the verified projects were fully completed. 3 were on-going.

(a) The On-Going Projects: The on-going projects in the Zone include;

- i. Provision of Infrastructure (Sewage at Federal Secretariat, Porthacourt, Rivers State)
- ii. Rehabilitation and Maintenance of the Fire Fighting System at Federal Secretariat Porthacourt Rivers State
Completion of Construction of Federal Secretariat Complex, Yenegoa, Bayelsa State awarded to M/S Trenur Nig. Ltd.

CHALLENGES

The following factors were found to have hindered the effective execution and performances of most of the projects monitored;

- (a) Security Challenges: Some projects in the states could not be verified due to security challenges. The affected projects have been listed at paragraph 4B of this summary.
- (b) Projects` Files: The Monitoring team could not locate some of the project files. Hence it became difficult to source required information on the projects affected. For example, most of the files for the Special Project Unit (SPU) and Engineering Services were said to be on transit and all efforts to get them failed.
- (c) The location of some projects listed for verification were not known to the Field Office Controllers. This made it impossible for the Monitoring Teams to verify those projects. The affected projects include:
 - i. Construction of a Block of Classroom at Erhuhur Primary School Akoko-Edo awarded to Tested Engineering Construction Limited
 - ii. Construction of Maternity at Ofukpo-Ekperi Etsako Central LGA Edo North Senatorial District awarded to M/S Nalot Multisystems Ltd
 - iii. Provision of Motorized Borehole in Yenegoa awarded to M/S Mulserve Limited
- (d) Some of the projects completed in 2019 which were yet to be handed over to the host Communities were in various degrees of deterioration. Example included; Completed Maternity center in Egeonu Etsako west LGA Edo North Senatorial District Edo State and Completed Maternity in Iyuku Esako West LGA Edo North Senatorial District Edo State.
- (e) A number of completed projects already handed over to the beneficiaries were not in use and they are already deteriorating. One of the reasons given for this situation by the beneficiaries interviewed was that funds are not available

for the servicing and fuelling the pumping machine for the Motorized Borehole. Some of such projects include Provision of Motorized Borehole at Federal Secretariat Complex Asaba Delta State, Contraction of deep well Borehole at Ozoro Delta State.

- (f) A number of completed projects were poorly constructed this has lead to the failure of these projects. Some of the reasons given for this by some field office staff was that there were no project vehicles and project Administration fund for effective supervision of projects. Some of such project is the Construction of Block of 6 Classrooms at Afowa Primary School Etsako West LGA, Edo North Senatorial District

RECOMMENDATIONS

Based on the foregoing observations and challenges the team recommended as follows:

- (a) Projects implementing Departments should as a matter of policy, make Project Files available to the Planning, Research and Statistics Department on request during monitoring exercise.
- (b) Utility vehicles and Project Administration fund should be provided whenever projects are awarded in the States to enable field officers supervise projects effectively.
- (c) Appropriate steps should be taken to ensure that completed projects are handed over to the host communities without delay in order to avoid theft and vandalization of the projects.
- (d) There is need to sensitize beneficiaries or host Communities on the importance of projects cited in their Communities and how the completed projects should be put into use to avoid deterioration.
- (e) The team may be directed to Verify National Housing Programme and revisit those projects that could not be located and those that were on-going during this monitoring tour.

The Monitoring and Evaluation exercise was coordinated by Mr O .B Ode - Martins, Director Planning, Research and Statistics and names of officers and the Projects sites visited are listed below .

S/N	NAME OF OFFICERS	DEPT.	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	Idris Mohammed	HRM	38	36	2	Member	North west
2	Atabo A. onduwa	Engineering Services				Member	
3	Zakariyau` Mohammed.M	PRS				Member	
4	Afiniki Yerima	PRS				Member	
5	Aminu Fadila B.	PRS				Member	
6	Yahaya Salihu	Finance & Accounts				Member	

S/N	NAME OF OFFICERS	DEPT	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	AHMED DUNOMA	PRS	31	27	Nil	Member	South West
2	OMONIYI TAIWO	PRS				Member	
3	Asipade Michael	PRS				Member	
4	Mohammad musa E.	PRS				Member	
5	ROSELYN APATA	PRS				Member	
6	Oloyede O. K	SPU				Member	

S/N	NAME OF OFFICERS	DEPT	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	Abdul Azeez M	PRS	42	37	5	Member	North Central
2	Panni Rosemary	Procurement				Member	
3	Mahammed Danladi	Library				Member	
4	Rakiya Haruna	Spu				Member	
5	Rosemary Wanniko	Highways				Member	

S/N	NAME OF OFFICERS	DEPT.	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	ONYETENU J.E	PRS	29	18	11	Member	South East
2	CHIKE S. OBIAKOR	PBH				Member	
3	IKENNA SMART	PRS				Member	
4	VITALIS NWAKPA	PRS				Member	
5	Okorie vitus	PRS				Member	

S/N	NAME OF OFFICERS	DEPT.	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	EZODE AUGUSTINE	PRS	25	18	7	Member	South South
2	NONGO DANIEL	ICT				Member	
3	IKENNA SMART	PRS				Member	
4	OGBOBULA OARE LESLY	PRS				Member	
5	UDOSEN SUSAN	PRS				Member	

S/N	NAME OF OFFICERS	DEPT.	NO OF PROJECTS IN EACH ZONE	PROJECT SITES VISITED	PROJECTS SITES NOT VISITED	POSITION	ZONES
1	SARAH DANIE L A	Library	35	28	7	Member	North East
2	MUSTAPHA S.U	PRS				Member	
3	IDRIS ISA	PRS					
4	MRS GIDADO H.	PRS				Member	
5	AHMED HASSAN	PRS				Member	
6	BALA JUBRIL	PRS				Member	

1.0 GEO-POLITICAL ZONE:

NORTH-CENTRAL

STATE:

FCT

LGA:

AMAC

LOCATION:

MABUSI, ABUJA

PROJECT TITLE:

**PROVISION OF ENGINEERING WORKSHOP
TOOLS (MECH)**

STATUS OF PROJECT: COMPLETED (100%)

NAME OF CONTRACTOR:

**MESSRS MAXWELL INTERNATIONAL
VENTURE LTD**

DATE OF AWARD:

27TH DECEMBER, 2019

CONTRACT SUM:

N12,000,000.00

PROJECT IMPACT ASSESSMENT:

FOR EFFECTIVE EFFICIENT JOB DELIVERY.



1.01 GEO-POLITICAL ZONE:
STATE:
LGA:
LOCATION:
PROJECT TITLE:

NORTH-CENTRAL
FCT
AMAC
MABUSHI, ABUJA
REPAIR OF FOULTY EQUIPEMENT AT
THE 2.5MVA/33/11KVTRANSFORMER
SUBSTATION IN FMWH PREMISES
COMPLETED (100%)
MESSRS AISRIL GLOBAL INV LTD
7TH FEBRUARY, 2020
N4,464,600.00
FOR EFFICIENT AND CONSTANT
POWER SUPPLY TO THE MINISTRY.

STATUS OF PROJECT:
NAME OF CONTRACTOR:
DATE OF AWARD:
CONTRACT SUM:
PROJECT IMPACT ASSESSMENT:



1.02 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

NORTH-CENTRAL

FCT

AMAC

MABUSHI, ABUJA

**REHABILITATION OF EXISTING
FIRE FIGHTING AND EARLY WARNING
SYSTEM AT THE FMW&H
(H) HEADQUARTERS, MABUSI AND KEY
INSTALLATIONS; FIRE ALARM, SMOKE
DETECTOR SYSTEM ETC (ELECTRICAL)**

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:


COMPLETED (100%)

**MESSRS NEXTON CONTRUCTION
LTD**

19TH DECEMBER, 2019

N6,520,015.50

**TO SAFEGUARD AND PROTECT THE
MINISTRY FROM FIRE OUTBREAK**

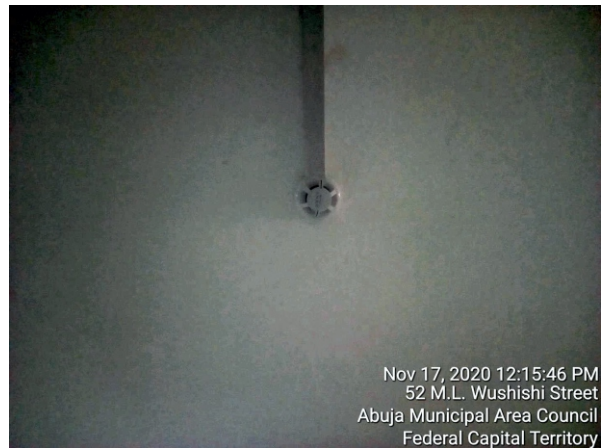

1.03 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

NORTH-CENTRAL

FCT

AMAC

MABUSHI, ABUJA

REHABILITATION OF EXISTING FIRE FIGHTING AND EARLY WARNING SYSTEM AT THE FMW&H (H) HEADQUARTERS, MABUSHI AND KEY INSTALLATIONS; FIRE ALARM, SMKE DETECTOR SYSTEM ETC (ELECTRICAL)

STATUS OF PROJECT:

COMPLETED (100%)

NAME OF CONTRACTOR:

MESSRS SUMFEM INTERNATIONAL LTD

DATE OF AWARD:


19TH DECEMBER, 2019

CONTRACT SUM:

N9,500,000.00

PROJECT IMPACT ASSESSMENT:

TO SAFEGUARD AND PROTECT THE MINISTRY FROM FIRE OUTBREAK

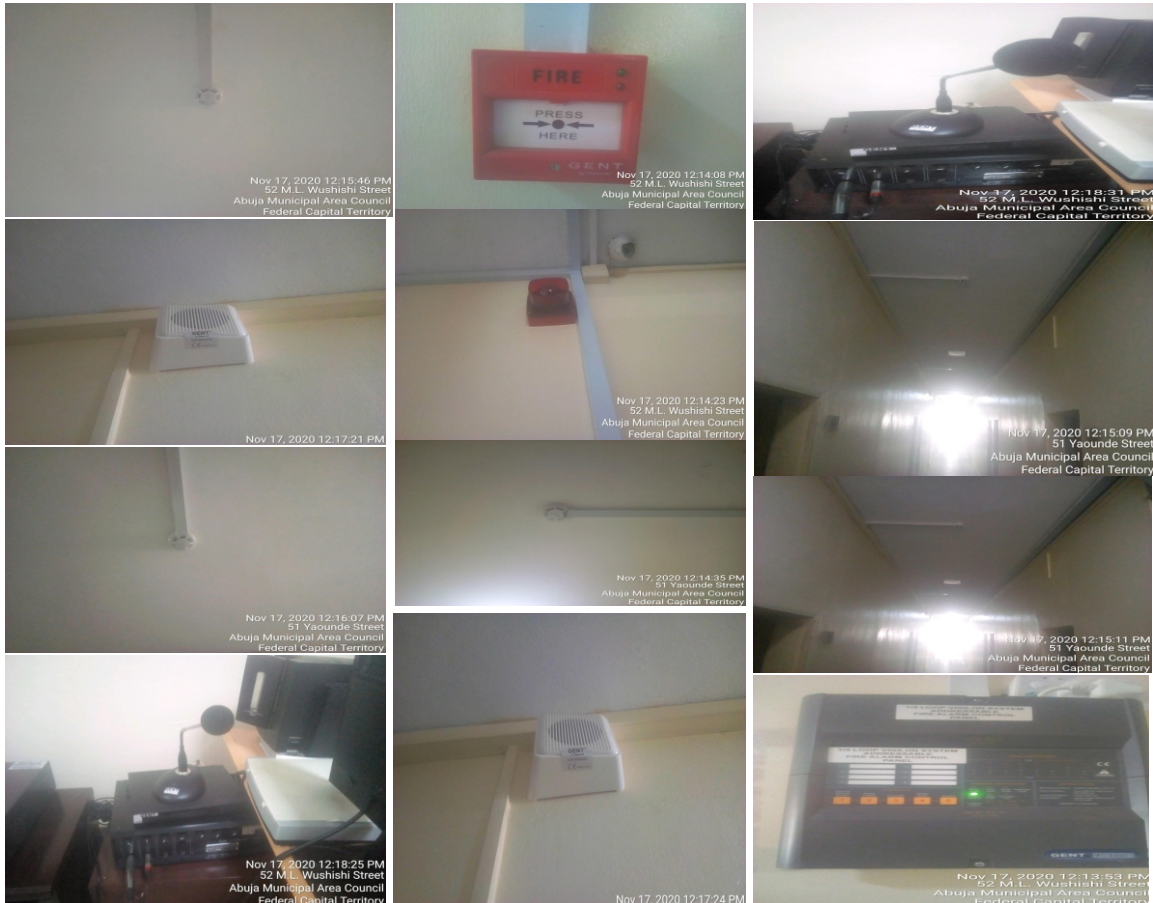

1.04 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

NORTH-CENTRAL

FCT

AMAC

MABUSHI ABUJA

**BUILDING ENERGY EFFICIENCY CODE
(BEEC)**


COMPLETED (100%)

M/S DIGMA INTERGRATED SERVICES LTD

27TH DECEMBER, 2019

N9,261,000.00

**CREATING AWARENESS TO THE MINISTRY
STAFFS.**

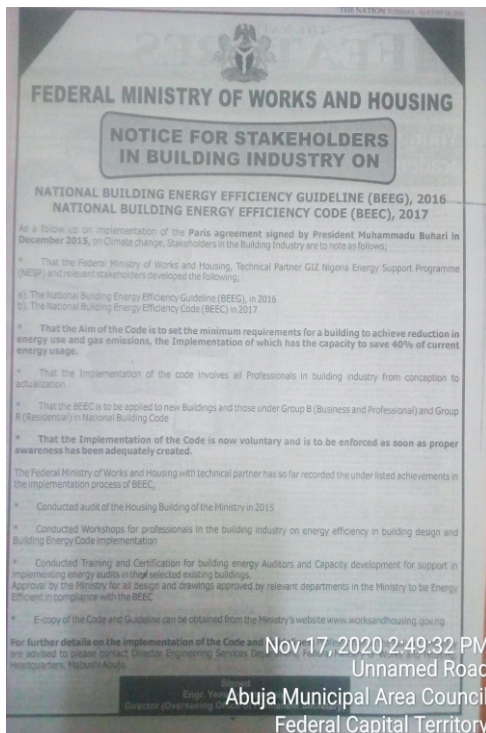

2.0 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	
PROJECT LOCATION:	BARIKIN SALE ALONG WAKILI MARKET
PROJECT TITLE:	CONSTRUCTION OF MOTORIZED BOREHOLE
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS FULUS SYNERGY LIMITED
DATE OF AWARD:	9TH DECEMBER, 2019
CONTRACT SUM:	N10,187,100.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY




2.01 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	BIDA LGA
PROJECT LOCATION:	ANIKE PRIMARY SCHOOL BIDA LOCAL GOVERNMENT
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BOREHOLE
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS BP SANY CO. NIGERIA LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY



2.02 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	MINNA
PROJECT LOCATION:	DUTSEN KURA CHACHANGA
PROJECT TITLE:	CONSTRUCTION OF ROADS, DRAINS AND CULVERT
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS NORTON INNOVATIVE SERVICES LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N147,627,192.31
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY



2.03 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	WUSHISI LGA
PROJECT LOCATION:	KUSADA MASALLACIN YANIZAL EMI WORO.
PROJECT TITLE:	PROVISION OF 500KVA TRANSFORMER
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS JOMIRAPH INTERNATIONAL LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N13,000,000.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY

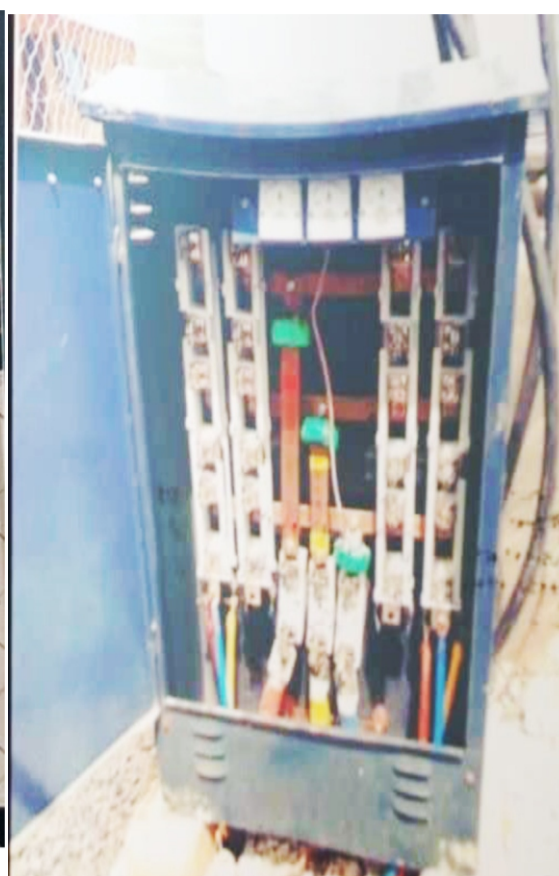

2.04 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	KONTAGORA LGA
PROJECT LOCATION:	NAMASKA ORPHANAGE SCHOOL KONTAGORA
PROJECT TITLE:	PROVISION OF SOLAR POWERED BOREHOLE
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS DALISHOW NIGERIA LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY



2.05 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	KONTAGORA LGA
PROJECT LOCATION:	ALMAJIRI SCHOOL CHIEF IMAM HOUSE RAMI, KONTAGORA
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 3- CLASSROOM
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS GOLD BIRD MULTI-TRADE LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N14,000,000.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY



2.06 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	NIGER STATE
LOCAL GOVERNMENT:	BIDA LGA
PROJECT LOCATION:	TAKO YANMABISHE-EMIKOTSU NASARAFU WARD, BIDA
PROJECT TITLE:	CONSTRUCTION OF MOTORIZED BOREHOLE
STATUS OF PROJECT:	100% COMPLETED
NAME OF CONTRACTOR:	MESSRS MALLAM MAJA NIGERIA LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
CONTRACT SUM:	N11,000,000.00
PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE SOCIO-ECONOMIC STATUS OF THE COMMUNITY



3.0 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	KOGI
LOCAL GOVERNMENT:	LOKOJA
PROJECT LOCATION:	FEDERAL MINISTRY OF WORKS AND HOUSING FIELD OFFICE LOKOJA, KOGI STATE
PROJECT TITLE:	PROVISION OF INFRASTRUCTURE (WATER) SPECIAL INTERVENTION PROGRAM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	CRYSTAL WORLD STANDARD
DATE OF AWARD	27-12-2019
CONTRACT SUM:	22,731,698.57
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



3.01 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	KOGI
LOCAL GOVERNMENT:	KOTON-KARFE
PROJECT LOCATION:	AHOKO
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH FURNITURE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	STEEL PILLAR DESIGN AND CONSTRUCTION LIMITED
DATE OF AWARD	27-12-2019
CONTRACT SUM:	42,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



12 Nov 2020 18:27:25



12 Nov 2020 18:27:43



12 Nov 2020 18:28:10



12 Nov 2020 18:28:36

3.02 GEOPOLITICAL ZONE:	NORTH CENTRAL
STATE:	KOGI
LOCAL GOVERNMENT:	KOTONKARFE
PROJECT LOCATION:	CHIKARA
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH FURNITURE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	STEEL PILLAR DESIGN AND CONSTRUCTION LIMITED
DATE OF AWARD	27-12-2019
CONTRACT SUM:	42,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



12 Nov 2020 18:51:59



12 Nov 2020 18:52:05



12 Nov 2020 18:52:54



12 Nov 2020 18:52:15

3.03 GEOPOLITICAL ZONE: NORTH CENTRAL

STATE: KOGI

LOCAL GOVERNMENT: KOTON- KARFE

PROJECT LOCATION: OZI

PROJECT TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS WITH FURNITURE

STATUS OF PROJECT: COMPLETED

NAME OF CONTRACTOR: STEEL PILLAR DESIGN AND CONSTRUCTION LIMITED

DATE OF AWARD 27-12-2019

CONTRACT SUM: 42,000,000.00

PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING

GEOPOLITICAL ZONE: NORTH CENTRAL



3.04 STATE:

LOCAL GOVERNMENT:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

KOGI

ADAVI

ADAVI

CONSTRUCTION OF DEEP WELL BOREHOLE

COMPLETED

TRUETECH GLOBAL INVESTMENT SERVICES LIMITED

27-12-2019

83,000,000.00

THE PROJECT IS FUNCTIONING



3.05 GEOPOLITICAL ZONE: NORTH CENTRAL
STATE: KOGI
LOCAL GOVERNMENT: DEKINA
PROJECT LOCATION: DEKINA
PROJECT TITLE: CONSTRUCTION OF DEEP WELL BOREHOLE
STATUS OF PROJECT: NOT COMPLETED
NAME OF CONTRACTOR: TRUETECH GLOBAL INVESTMENT SERVICES LIMITED
DATE OF AWARD 27-12-2019
CONTRACT SUM: 83,000,000.00
PROJECT IMPACT ASSESSMENT: THE PROJECT IS NOT FUNCTIONING



3.06 GEOPOLITICAL ZONE: NORTH CENTRAL

STATE: KOGI

LOCAL GOVERNMENT: IMANI

PROJECT LOCATION: IMANI

PROJECT TITLE: CONSTRUCTION OF DEEP WELL BOREHOLE

STATUS OF PROJECT: COMPLETED

NAME OF CONTRACTOR: TRUETECH GLOBAL INVESTMENT SERVICES LIMITED

DATE OF AWARD 27-12-2019

CONTRACT SUM: 83,000,000.00

PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING



3.07	GEOPOLITICAL ZONE:	NORTH CENTRAL
	STATE:	KOGI
	LOCAL GOVERNMENT:	OKENE
	PROJECT LOCATION:	OKENE
	PROJECT TITLE:	CONSTRUCTION OF DEEP WELL BOREHOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	TRUETECH GLOBAL INVESTMENT SERVICES LIMITED
	DATE OF AWARD	27-12-2019
	CONTRACT SUM:	83,000,000.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



11 Nov 2020 18:35:05




11 Nov 2020 18:31:29



11 Nov 2020 18:34:39




11 Nov 2020 18:33:05

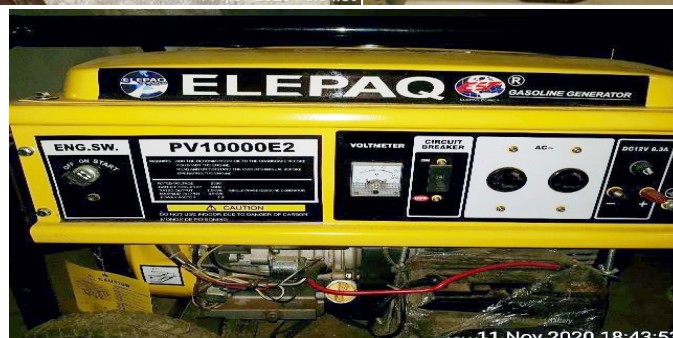

12V 11, Nov, 2020 18:43:53

3.08 GEOPOLITICAL ZONE: NORTH CENTRAL
STATE: KOGI
LOCAL GOVERNMENT: OYENYI
PROJECT LOCATION: OYENYI
PROJECT TITLE: CONSTRUCTION OF DEEP WELL BOREHOLE
STATUS OF PROJECT: COMPLETED
NAME OF CONTRACTOR: TRUETECH GLOBAL INVESTMENT SERVICES LIMITED
DATE OF AWARD 27-12-2019
CONTRACT SUM: 83,000,000.00
PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING

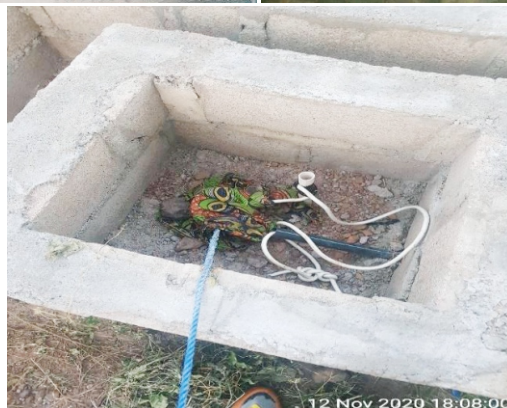

4.0 GEO-POLITICAL ZONE: NORTH-CENTRAL
STATE: NASARAWA
LGA: LAFIA
LOCATION: FARIN KASA ROAD LAFIA
PROJECT TITLE: CONTRUCTION OF ONE BLOCK OF THREE CLASSROOMS AT IMAM DAHIRU ALMAJIRI SCHOOL

STATUS OF PROJECT: COMPLETED(100%)
NAME OF CONTRACTOR: MESSRS DIDOL AND MAHOL NIG. LTD
DATE OF AWARD: 27TH DECEMBER, 2019
CONTRACT SUM: N14,000,000.00
PROJECT IMPACT ASSESSMENT: THE PROJECT WILL OPPORTUNITY FOR THE ALMAJIRI TO BOTH WESTERN AND ISLAMIC KNOWLEDGE. THE ALMAJIRIES WERE NOT ON GROUND AS AT THE TIME OF THE MONITORING TO HAVE PROJECT IMPACT ASSESSMENT FROM THEM.



4.01 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

NORTH-CENTRAL

NASARAWA

LAFIA

LAFIA

FEDERAL SECRETARIAT COMPLEX

ONGOING(54%)

MESSRS FAPLINS NIG. LTD

9TH NOVEMBER, 2011

N3,120,718,297.93

THE PROJECT WILL BRING THE PRESENT OF THE FEDERAL GOVERNMENT TO LAFIA AND THE STATE IN GENERAL, THEREFORE IT WILL PROVIDE JOB OPPORTUNITY TO THE PEOPLE OF THE STATE.



4.02 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

NORTH-CENTRAL

NASARAWA

KOKONA, KEFFI AND KARU

KANDELE IN KOKONA, JIGWADA IN KEFFI

AND MARARBA IN KARU

CONSTRUCTION OF 3NO SOLAR POWERED BOREHOLES

COMPLETED(100%)

MESSRS LANSOJ NIG. LTD

27TH DECEMBER, 2019

N34,999,998.90

THE PROJECT AFTER COMPLETION PROVIDED CLEAN AND GOOD DRINKING WATER TO THE COMMUNITIES, BUT UNFORTUNATELY, THE BOREHOLE AT KANDELE IN KOKONA AND JIGWADA IN KEFFI HAVE STOP WORKING EXCEPT THE ONE AT MARARABA IN KARU THAT IS FUNCTIONAL AS AT THE TIME OF THE



4.03 GEO-POLITICAL ZONE:

STATE:

LGA:

LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

NORTH-CENTRAL

NASARAWA

KARU

KUDU, ASO KODOPE KARU LGA

PROVISION OF 1NO SOLAR POWERED BOREHOLE

COMPLETED(100%)

MESSRS ONE NATION ENERGY PLATFORM LTD

27TH DECEMBER, 2019

N11,666,666.66

PEOPLE OF THE COMMUNITY ARE VERY HAPPY WITH THE GOVERNMENT FOR PROVIDING THE BOREHOLE.



5.0 GEO-POLITICAL ZONE:	NORTH CENTRAL
STATE:	PLATEAU
L.G.A:	BOKKOS
PROJECT LOCATION:	DAFFO TOWN, DAFFO DISTRICT
PROJECT TITLE:	PROVISION OF MOTORIZED BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	PRIME FORTUNE NIGERIA LIMITED.
DATE OF AWARD:	27TH DECEMBER, 2019
CONTRACT SUM:	N10,187,100.00
IMPACT ASSESSMENT:	



Nov 3, 2020 2:08:23 PM



Nov 3, 2020 2:09:07 PM



Nov 3, 2020 2:09:56 PM

5.01 GEO-POLITICAL ZONE: NORTH CENTRAL
STATE: PLATEAU
L.G.A: PANKSHIN
PROJECT LOCATION: CHIKAN CHIAGWONG
PROJECT TITLE: PROVISION OF SOLAR POWERED BOREHOLE
STATUS PROJECT: COMPLETED
NAME OF CONTRACTOR: MANYKA BUSINESS NETWORK LTD.
DATE OF AWARD: 27TH DECEMBER, 2019
CONTRACT SUM: ₦ 11,666,666.00
IMPACT ASSESSMENT:



5.02 GEO-POLITICAL ZONE:

NORTH CENTRAL

STATE:

PLATEAU

L.G.A:

KANKE

PROJECT LOCATION:

**L.E.A PRIMARY SCHOOL KUKSUR,
MWELL II**

PROJECT TITLE:

**CONSTRUCTION & FURNISHING OF BLOCK
OF 3 CLASSROOM**

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

BATUL FARMS LTD.

DATE OF AWARD:

27TH DECEMBER, 2019

CONTRACT SUM:

₦12,965,400.00

IMPACT ASSESSMENT

- A. INCREASE IN SCHOOL ENROLMENT
- B. CONDUCIVE ENVIRONMENT FOR LEARNING
- C. ACCESS TO QUALITATIVE EDUCATION



5.03 GEO-POLITICAL ZONE: **NORTH-CENTRAL**

STATE: **PLATEAU**

L.G.A: **PANKSHIN**

PROJECT LOCATION: **G.S.S KOR**

PROJECT TITLE: **CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS**

STATUS OPROJECT:

NAME OF CONTRACTOR: **COSNUEL INVESTMENT LTD.**

DATE OF AWARD: **27TH DECEMBER, 2019**

CONTRACT SUM: **₦14,000,000.00**

IMPACT ASSESSMENT:

- A. INCREASE IN SCHOOL ENROLMENT
- B. ACCESS TO QUALITY EDUCATION
- C. LEAVING UNDER CONDUCIVE ENVIRONMENT.



5.04 GEOPOLITICAL ZONE: NORTH-CENTRAL
STATE: PLATEAU
L.G.A:

A. BOKKOS L.G.A
B. MANGUS L.G.A

PROJECT LOCATION:

A. G.S.S. HOROP
B. G.S.S. PUSHIT

PROJECT TITLE:

CONSTRUCTION AND FURNISHING OF 2 BLOCKS
OF 3 CLASSROOMS

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

TOMLAD NIG. LTD.

DATE OF AWARD:

22ND DECEMBER, 2019

CONTRACT SUM:

₦25,930,800.00

IMPACT ASSESSMENT:

- A. INCREASE IN SCHOOL ADMISSION
- B. CONDUCIVE ENVIRONMENT FOR LEARNING
- C. ACCESS TO QUALITATIVE EDUCATION

G.S.S. HOROP



G.S.S. PUSHIT



6.0 GEO-POLITICAL ZONE: NORTH-CENTRAL

STATE: BENUE

L.G.A: GBBOKO

PROJECT LOCATION: C.S.S PIKA

PROJECT TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS

STATUS OF PROJECT: COMPLETED

NAME OF CONTRACTOR: KULOS TECHNOLOGIES LTD.

DATE OF AWARD: 29TH MARCH, 2019

CONTRACT SUM: ₦14,000,000.00

IMPACT ASSESSMENT:

- A. INCREASE IN SCHOOL ADMISSION
- B. MAKES LEARNING EASIER AND BETTER UNDER FAVOURABLE ENVIRONMENT



6.01 GEO-POLITICAL ZONE:	NORTH - CENTRAL
STATE:	BENUE
L.G.A:	MAKURDI
PROJECT LOCATION:	FEDERAL SECRETARIAT, MAKURDI
PROJECT TITLE:	RESTORATION OF OFFICE ENVIRONMENT
STATUS OF PROJECT:	LIGHTING COMPLETED
NAME OF CONTRACTOR:	NUBNA NIG. LTD.
DATE OF AWARD:	27 TH DECEMBER, 2019
CONTRACT SUM:	₦13,177,500.00
IMPACT ASSESSMENT:	

A. ENHANCE THE SECURITY OF THE PREMISES

B. ENABLE THE SECURITY OF OFFICERS TO PERFORM THEIR DUTIES EFFECTIVELY AND EFFICIENTLY



6.02 GEO - POLITICAL ZONE: **NORTH CENTRAL**

STATE: **BENUÉ**

L.G.A: **MAKURDI**

PROJECT LOCATION: **FEDERAL SECRETARIAT, MAKURDI**

PROJECT TITLE: **REHABILITATION OF AIR CONDITIONER AND REFRIGERATORS**

STATUS OF PROJECT: **COMPLETED**

NAME OF CONTRACTOR: **G.S.E.S. NIG. LTD.**

DATE OF AWARD: **27TH DECEMBER, 2019**

CONTRACT SUM: **₦4,537,890.00**

IMPACT ASSESSMENT: **A CONDUCTIVE WORKING ENVIRONMENT**



6.03 GEO-POLITICAL ZONE: NORTH-CENTRAL
STATE: BENUE
L.G.A: MAKURDI
PROJECT LOCATION: FEDERAL SECRETARIAT, MAKURDI
PROJECT TITLE: PROVISION OF SOLAR POWERED BOREHOLE
STATUS OF PROJECT: COMPLETED
NAME OF CONTRACTOR: NIPHEMY SOLUTIONS LIMITED
DATE OF AWARD: 27TH DECEMBER, 2019
CONTRACT SUM: ₦11,666,666.00

IMPACT ASSESSMENT:

- A. ACCESS TO CLEAN AND PORTABLE WATER BY THE STAFF
- B. ENHANCES CLEAN ENVIRONMENT THAT GUARANTEE HEALTHY LEAVING
- C. THE CLEANERS PERFORM THEIR DUTIES WITH EASE.



6.04 GEO-POLITICAL ZONE: NORTH CENTRAL
STATE: BENUE
L.G.A:

- A. APA LGA
- B. GWER EAST LGA
- C. GWER WEST LGA

PROJECT LOCATION

- A. ISLAMIYA PRIMARY SCHOOL OFOKE-OJOPE
- B. G.D.S.S. ALIADE
- C. G.C.S.S. NAKA

PROJECT TITLE: CONSTRUCTION OF 3 BLOCKS OF 3 CLASSROOMS
STATUS OF PROJECT: COMPLETED
NAME CONTRACTOR: TOMLAD NIG. LTD.
DATE OF AWARD: 22ND DECEMBER, 2019
CONTRACT SUM: ₦38,896,200.00

- IMPACT ASSESSMENT:**
- A. ACCESS TO QUALITY EDUCATION
 - B. LEARNING UNDER CONDUCIVE ENVIRONMENT
 - C. INCREASE IN SCHOOL ENROLMENT
 - D. PROVIDE ROOMS FOR LIBRARY, LABORATORY AND STAFF ROOM AS WELL

ISLAMIYYA PRIMARY SCHOOL, OFOKE-OJOPE



G.D.S.S ALIADE



G.C.S.S. NAKA



6.05 GEO-POLITICAL ZONE: NORTH-CENTRAL
STATE: BENUE STATE
L.G.A: KONSHISHA LGA
PROJECT LOCATION:
 A. WUESE
 B. GBOGBO
 C. KORINYA
PROJECT TITLE: CONSTRUCTION AND RENOVATION OF
 COMMUNITY COUNCIL HALL
STATUS OF PROJECT: COMPLETED
NAME OF CONTRACTOR: SALMAN FARUK NIG. LTD.
DATE OF AWARD: 27TH DECEMBER, 2019
CONTRACT SUM: ₦69,457,500.00

IMPACT ASSESSMENT:

- A. IT HELPS IN PRESERVATION OF CULTURAL HERITAGE
- B. IT PROVIDES AN ENABLING ENVIRONMENT FOR SOCIAL AND POLITICAL ACTIVITIES OF THE TRADITIONAL SET UP.

COMMUNITY HALL WUESE



COMMUNITY HALL GBOGBO



COMMUNITY HALL KORINYA



7.0 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: EDU
LOCATION: SHARAGI
TITLE: PROCUREMENT AND INSTALLATION OF 500KVA TRANSFORMER

STATUS: INSTALLED BUT NOT CONNECTED
NAME OF CONTRACTOR: COCASET NIG. LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N13,000,000.00
IMPACT ASSESSMENT: TO DISTRIBUTE AND IMPROVE QUALITY OF ELECTRICITY SUPPLY IN COMMUNITY.



7.01 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: OWU ISIN
LOCATION: IWO ISIN
TITLE: PROVISION OF SOLAR POWERED BOREHOLE
STATUS: COMPLETED AND FUNCTIONING WELL
NAME OF CONTRACTOR: HAMICK INVESTMENT. LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N13,666,666.00
IMPACT ASSESSMENT: PROVISION OF SAFE AND HEALTHY DRINKING

WATER, IT REDUCED OR ERADICATE WATER BORN DISEASES.



7.02 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: ILORIN SOUTH
LOCATION: ILORIN
TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS
STATUS: COMPLETED AND IN USE
NAME OF CONTRACTOR: BLESSED ARABA 1 INVESTMENT LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N14,000,000.00
IMPACT ASSESSMENT: CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY


TO THE SCHOOL AND CREATE GOOD ENVIRONMENT FOR LEARNING, THE PEOPLE OF THE COMMUNITY WERE HAPPY HAVING THE PROJECT IN THEIR MIST.



7.03 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: ILORIN SOUTH
LOCATION: ILORIN
TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS
STATUS: COMPLETED AND IN USE
NAME OF CONTRACTOR: TOAD GLOBAL RESOURCES LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N14,000,000.00
IMPACT ASSESSMENT: CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY TO THE SCHOOL AND CREATE GOOD ENVIRONMENT FOR LEARNING.



7.04 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: OYUN
LOCATION: IPEE
TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS
STATUS: COMPLETED AND IN USE
NAME OF CONTRACTOR: BARRACUDA NIG LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N14,000,000.00
IMPACT ASSESSMENT: CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY TO THE SCHOOL AND CREATE GOOD ENVIRONMENT FOR LEARNING, HAPPY HAVING THE PROJECT AMONG THEM.



7.05 ZONE: NORTH CENTRAL
STATE: KWARA
LGA: PATEGI
LOCATION: EGWA
TITLE: CONSTRUCTION OF A BLOCK OF 2 CLASSROOMS
STATUS: COMPLETED AND IN USE
NAME OF CONTRACTOR: JOYDRILL INTEGRATED SERVICES LTD
DATE OF AWARD: 27/ 12/2019
CONTRACT SUM: N11,000,000.00
IMPACT ASSESSMENT: CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY TO THE COMMUNITY, CREATE GOOD AND CONDUCIVE, ENVIRONMENT FOR LEARNING, IT HAS REMOVE THE STRESS OF GOING TO THE NEIGHBOURING COMMUNITY TO ACCESS EDUCATION, BROUGHT JOY TO THE COMMUNITY. (THE FIRST TIME THEY HAVE SCHOOL IN THIS COMMUNITY).



7.06 ZONE:	NORTH CENTRAL
STATE:	KWARA
LGA:	PATEGI
LOCATION:	PATEGI
TITLE:	CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS
STATUS:	COMPLETED AND IN USE
NAME OF CONTRACTOR:	VAGRIDA NIGERIA LTD
DATE OF AWARD:	27/ 12/2019
CONTRACT SUM:	N14,000,000.00
IMPACT ASSESSMENT:	CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY TO THE COMMUNITY, CREATE GOOD AND CONDUCTIVE, ENVIRONMENT FOR LEARNING.



8.0 GEOPOLITICAL ZONE: NORTH EAST
STATE: ADAMAWA
LOCAL GOVERNMENT AREA L.G.A: YOLA SOUTH
PROJECT LOCATION: FEDERAL SECRETARIAT YOLA ADAMAWA STATE
STATUS OF PROJECT: COMPLETED
NAME OF CONTRACTOR: DAIMON SQUAR LIMITED
DATE OF AWARD: 27TH DECEMBER, 2019
CONTRACTOR SUM: 24,000,000.00
PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING



8.01 GEOPOLITICAL ZONE.	NORTH EAST
STATE.	ADAMAWA
LOCAL GOVERNMENT AREA L.G.A.	YOLA SOUTH
PROJECT LOCATION.	FEDERAL SECRETARIAT YOLA ADAMAWA STATE
STATUS OF PROJECT.	COMPLETED
NAME OF CONTRACTOR.	JABAL ADVANCE NIG LTD
DATE OF AWARD.	27TH DECEMBER, 2019
CONTRACTOR SUM.	22,527,000.00
PROJECT IMPACT ASSESSMENT.	THE PROJECT IS FUNCTIONING



8.02 GEOPOLITICAL ZONE.	NORTH EAST
STATE.	ADAMAWA
LOCAL GOVERNMENT AREA L.G.A.	DEMSA LOCAL GOVERNMENT
PROJECT LOCATION.	ANGUWAN BALI, DEMSA TOWN
STATUS OF PROJECT.	COMPLETED
NAME OF CONTRACTOR.	NGOBARE VENTURES LIMITED
DATE OF AWARD.	27TH DECEMBER, 2019
CONTRACTOR SUM.	11,666,666.00
PROJECT IMPACT ASSESSMENT.	THE PROJECT IS FUNCTIONING



9.0	GEOPOLITICAL ZONE.	NORTH EAST
	STATE.	BAUCHI
	LOCAL GOVERNMENT AREA L.G.A.	TAFAWA BALEWA L.G.A
	PROJECT LOCATION.	NINGI AND WARJI
	PROJECT TITLE.	CONSTRUCTION OF DEEP WELL BOREHOLE
	STATUS OF PROJECT.	COMPLETED
	NAME OF CONTRACTOR.	M/S PRIME FORTUNE NIG.LTD
	DATE OF AWARD.	27TH DECEMBER, 2019
	CONTRACTOR SUM.	36,000,000.00
	PROJECT IMPACT ASSESSMENT.	THE PROJECT HAS IMPACTED POSITIVELY TO THE COMMUNITY



9.01 GEOPOLITICAL ZONE.
STATE.
LOCAL GOVERNMENT AREA L.G.A.
PROJECT LOCATION.
PROJECT TITLE

STATUS OF PROJECT.
NAME OF CONTRACTOR.
DATE OF AWARD.
CONTRACTOR SUM.
PROJECT IMPACT ASSESSMENT.

NORTH EAST
BAUCHI
 TAFAWA BALEWA L.G.A
 MWARI, BONGAH, SUM, MALAR, AND LUSA
 CONSTRUCTION OF BLOCK OF 3
 CLASSROOM WITH FURNITURES
COMPLETED
 M/S ZIMTAIN RESOURCES LTD
 18TH JANUARY, 2017
 92,595,000.00
 THE PROJECT HAS IMPACTED
 POSITIVELY TO THE COMMUNITY



**9.02 GEOPOLITICAL ZONE.
STATE.**

LOCAL GOVERNMENT AREA L.G.A.

PROJECT LOCATION.

PROJECT TITLE.

STATUS OF PROJECT.

NAME OF CONTRACTOR.

DATE OF AWARD.

CONTRACTOR SUM.

PROJECT IMPACT ASSESSMENT.

NORTH EAST

BAUCHI

TAFAWA BALEWA L.G.A

BAKARO/MAKAMA ROAD BAUCHI TOWN

SUPPLY AND INSTALLATION OF SOLAR STREET LIGHT


COMPLETED

M/S AMG NIGERIA LTD

2TH DECEMBER, 2019

27,500,000.00

THE PROJECT HAS IMPACTED
POSITIVELY TO THE COMMUNITY

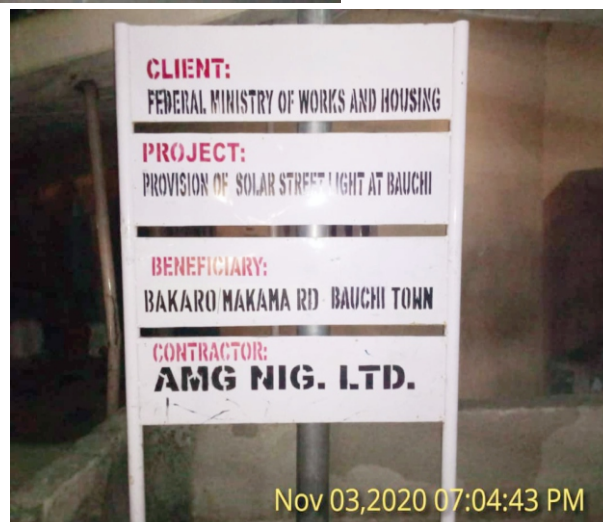

**9.03 GEOPOLITICAL ZONE.
STATE.**

LOCAL GOVERNMENT AREA L.G.A.

PROJECT LOCATION.

PROJECT TITLE.

STATUS OF PROJECT.

NAME OF CONTRACTOR.

DATE OF AWARD.

CONTRACTOR SUM.

PROJECT IMPACT ASSESSMENT.

NORTH EAST

BAUCHI

TAFAWA BALEWA L.G.A

ZWALL AND KUTARU, BAUCHI STATE

CONSTRUCTION OF 3 CLASSROOM BLOCK
WITH FURNITURES

COMPLETED

M/S ZIMTAIN RESOURCES LTD

18TH JANUARY, 2017

28,000,000.00

THE PROJECT HAS IMPACTED
POSITIVELY TO THE COMMUNITY



9.04 GEOPOLITICAL ZONE.
STATE.
LOCAL GOVERNMENT AREA L.G.A.
PROJECT LOCATION.
PROJECT TITLE.

STATUS OF PROJECT.
NAME OF CONTRACTOR.
DATE OF AWARD.
CONTRACTOR SUM.
PROJECT IMPACT ASSESSMENT.

NORTH EAST
BAUCHI
TAFAWA BALEWA L.G.A
BURGA, DULL, MBAT 1 AND 2 AT BAUCHI STATE
CONSTRUCTION OF BLOCK OF 3
CLASSROOM WITH FURNITING
COMPLETED
M/S AFDIN CONSTRUCTION LTD
18TH JANUARY, 2017
92,595,000.00
THE PROJECT HAS IMPACTED
POSITIVELY TO THE COMMUNITY



10.0 GEO- POLITICAL ZONE:
STATE:
LGA:
PROJECT LOCATION:
PROJECT TITLE:

NORTH EAST
BORNO
MAIDUGURI
HAUSARI WARD AND KALIARI WARD
CONSTRUCTION OF DEEPWELL
BOREHOLES.

STATUS OF PROJECT:
NAME OF CONTRACTOR:
DATE OF AWARD:
CONTRACT SUM:
PROJECT IMPACT ASSESMENT:

COMPLETED (100%)
HAWAWU GLOBAL VENTURES L I MI TED.
22-12-2019
N80,000,000.00
PROJECTS ARE FUNCTIONING.



10.01 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESMENT:

NORTH EAST

BORNO

MAIDUGURI

JIDDARI ARFO ROAD, MAIDUGURI

CONSTRUCTION OF MOTORIZED
BOREHOLES.

COMPLETED (100%)

NAKARAM ENTERPRISE LIMITED.

22-12-2019

N110,000,000.00

PROJECTS ARE FUNCTIONING



10.02 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	BORNO
LGA:	MAIDUGURI
PROJECT LOCATION:	GATUMARI WARD, MAIDUGURI
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BOREHOLES.
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	DIAMOND SUITES LIMITED.
DATE OF AWARD:	22-12-2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING.



10.03 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	BORNO
LGA:	MAIDUGURI
PROJECT LOCATION:	NGOMARI GANA , MAIDUGURI
PROJECT TITLE:	PROVISION OF SOLAR POWERED BOREHOLES.
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	MIRIAMAG CONSTRUCTION COMPANY LIMITED.
DATE OF AWARD:	22-12-2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING.



11.0 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	YOBE
LGA:	JAKUSKO
PROJECT LOCATION:	OLD DISPENSARY , JAKUSKO LGA, YOBE
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BOREHOLES.
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACT:	ORKABAG GLOBAL SERVICES LIMITED.
DATE OF AWARD:	29-12-2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING.



11.01 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	YOBE
LGA:	POTISKUM
PROJECT LOCATION:	LAYIN MAI UNGUWAR NAHUTA, POTISKUM, YOBE
PROJECT TITLE:	POVISION OF SOLAR POWERED BOREHOLES.
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	KARETO INTERNATIONAL LIMITED.
DATE OF AWARD:	29-12-2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING



11.02 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

NORTH EAST

YOBE

POTISKUM

KATIN WAJE AREA, POTISKUM, YOBE
CONSTRUCTION OF VA BLOCK OF THREE
CLASSROOM AND RENOVATION OF
SCHOOL .

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESMENT:

COMPLETED (100%)

SEFARU GLOBAL NIGERIA LIMITED.

29-12-2019

N22,000,000.00

PROJECTS ARE FUNCTIONING



11.03	GEO-POLITICAL ZONE:	NORTH EAST
	STATE:	YOBE
	LGA:	POTISKUM
	PROJECT LOCATION:	POTISKUM, YOBE
	PROJECT TITLE:	CONSTRUCTION OF A DEEPWELL BOREHOLE
	STATUS OF PROJECT:	COMPLETED (100%)
	NAME OF CONTRACTOR:	LRB GLOBAL NIGERIA LIMITED.
	DATE OF AWARD:	29-12-2019
	CONTRACT SUM:	N85,000,000.00
	PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING.



4 Nov 2020 14:28:43
Maiduguri-Potiskum Road
Potiskum
Yobe



4 Nov 2020 14:29:07
Maiduguri-Potiskum Road
Potiskum
Yobe

11.04 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	YOBE
LGA:	BADE WEST
PROJECT LOCATION:	ASBAK VILLAGE, YOBE
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWER BOREHOLE
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	ANTHONY MARIAFRED NIGERIA LIMITED.
DATE OF AWARD:	29-12-2019
CONTRACT SUM:	N11,666,666.00
PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING



11.05	GEO-POLITICAL ZONE:	NORTH EAST
	STATE:	YOBE
	LGA:	KARASUWA
	PROJECT LOCATION:	GARIN MAMMADU, YOBE
	PROJECT TITLE:	PROVISION OF SOLAR POWER BOREHOLE
	STATUS OF PROJECT:	COMPLETED (100%)
	NAME OF CONTRACTOR:	FFA CONTINENTAL CONCEPT LIMITED.
	DATE OF AWARD:	29-12-2019
	CONTRACT SUM:	N9,681,313.00
	PROJECT IMPACT ASSESMENT:	PROJECTS ARE FUNCTIONING.



12.0	GEO-POLITICAL ZONE:	NORTH EAST
	STATE:	GOMBE
	L.G.A:	BALLANGA
	PROJECT LOCATION:	BALLANGA VILLAGE
	PROJECT TITTLE:	PROVISION OF INO MOTORIZED BOREHOLE
	STATUS OF PROJECT:	100%
	NAME OF CONTRACTOR:	MUSA HASSAN UNIVERSAL VENTURE
	DATE OF AWARD:	27TH DECEMBER,2019
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS COMPLETED AND IN USE
	PROJECT COST:	N 11, 000,000.00



12.01 GEO-POLITICAL ZONE:

STATE:

L.G.A

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

PROJECT IMPACT ASSESSMENT:

PROJECT COST:

NORTH EAST

GOMBE

AKKO

ISLAMIYA SCHOOL IN TUMU

SUPPLY & INSTALLATION OF SOLAR STREET LIGHT IN TUMU



100%

M/S A3 INTERNET SOLUTION LTD.

27TH DECEMBER, 2019.

PROJECT COMPLETED AND IN USE

N26,000,000.00

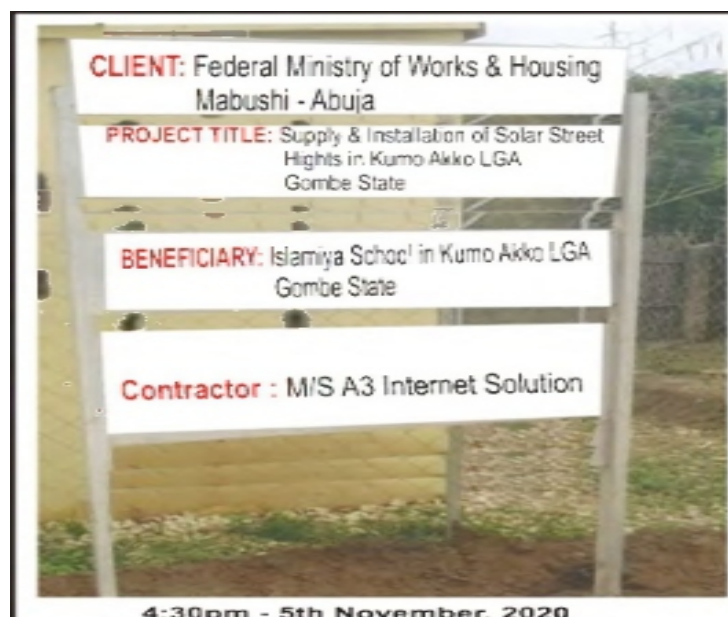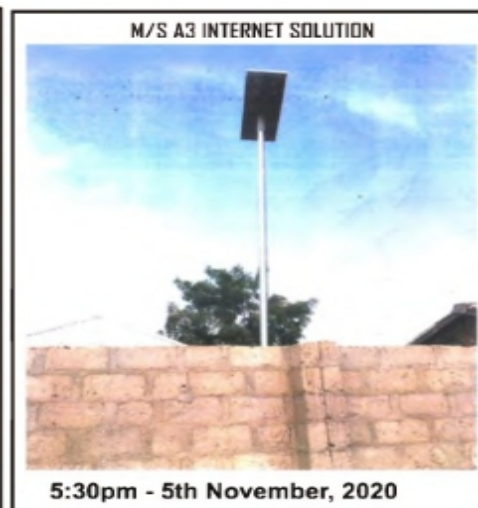

12.02 GEO-POLITICAL ZONE:	NORTH EAST
STATE:	GOMBE
L.G.A:	GOMBE
PROJECT TITLE:	CONSTRUCTION OF 2NOS SOLAR POWERED BOREHOLES
STATUS OF PROJECT:	100%
NAME OF CONTRACTOR:	M/S ASU GLOBAL VENTURES NIGERIA LIMITED
DATE OF AWARD:	27TH DECEMBER, 2019
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS COMPLETED AND IN USE
PROJECT COST:	N11,666,666.00



12.03 GEO-POLITICAL ZONE:

STATE:

L.G.A:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

PROJECT IMPACT ASSESSMENT:

PROJECT COST:

NORTH EAST

GOMBE

GOMBE

FEDERAL COLLEGE OF EDUCATION
(TECH)

SUPPLY AND INSTALLATION OF 25 Nos
SOLAR STREET LIGHTS

100%

M/S AMG NIGERIA LIMITED

27TH DECEMBER, 2019

THE PROJECT IS COMPLETED AND IN
USE

N 27,500,000.00



12.04 GEO-POLITICAL ZONE:

STATE:

L.G.A:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

PROJECT IMPACT ASSESSMENT:

PROJECT COST:

NORTH EAST

GOMBE

AKKO

AKKO FEDERAL CONSTITUENCY

**CONSTRUCTION OF SOLAR POWERED
BOREHOLE**

100%

M/S DOVEBELL LIMITED

27TH DECEMBER, 2019

THE PROJECT IS COMPLETED AND IN USE


N 11,666.666.00



4:30pm - 4th November, 2020



4:30pm - 4th November, 2020

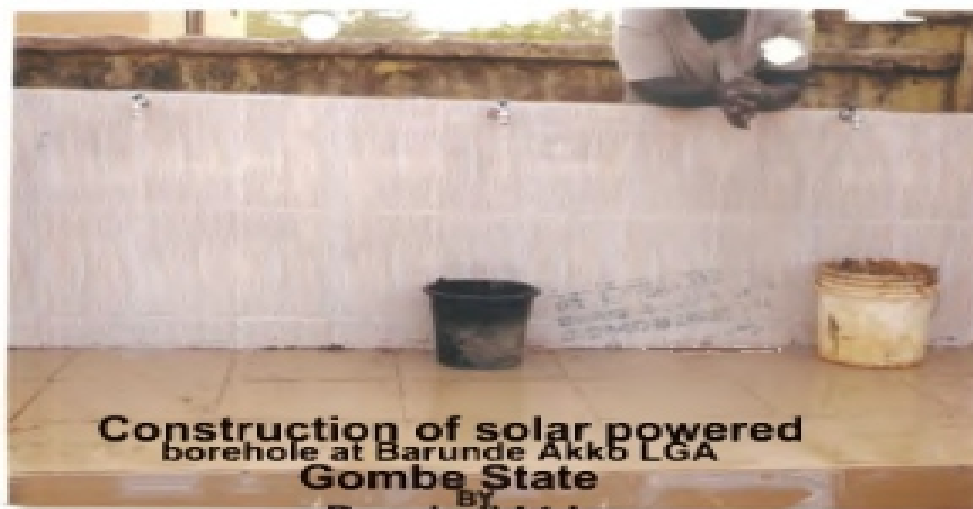

4:30pm - 4th November, 2020

13.0 GEOPOLITICAL ZONE:

STATE:

LOCAL GOVERNMENT:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

NORTH WEST

KANO

GAWUNA

GAWUNA

CONSTRUCTION OF 1 NO SOLAR POWERED BOREHOLE

COMPLETED

MIKEOA GLOBAL CONCEPT LTD.

27 - 12 - 2019

11,666,666.00

THE PROJECT IS FUNCTIONING



13.01 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	KANO
LOCAL GOVERNMENT:	NASARAWA LGA
PROJECT LOCATION:	GWAGWARWA
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	ZUGBWA SYNERGY NIGERIA LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	11,666,666.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



13.02 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	KANO
LOCAL GOVERNMENT:	NASARAWA LGA
PROJECT LOCATION:	BASHIR DALHATU ROAD, OFF MAIDUGURI ROAD, HOTORO GRA
SWPROJECT TITLE:	SUPPLY AND INSTALLATION OF SOLAR STREET LIGHT
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	NASA GLOBAL RESOURCES SERVICE LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	110,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



13.03 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

KANO

LOCAL GOVERNMENT:

KUMBOTSO LGA

PROJECT LOCATION:

ZAWACIKI HOUSING ESTATE, PANSHEKARA

PROJECT TITLE:

**ROAD, KUMBOTSO LGA
PROVISION PF SOLAR POWERED
BOREHOLE**

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

ECHO AND LGA ENGINEERINA NIG. LTD.

DATE OF AWARD:

27 - 12 - 2019

CONTRACT SUM:

11,666,666.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



13.04 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

KANO

LOCAL GOVERNMENT:

TSANYAWA LGA

PROJECT LOCATION:

TSANYAWA-GURUN-NASARAWA ROAD

PROJECT TITLE:

CONSTRUCTION OF ROAD/DRAINAGE AND

BRIDGE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

ALMUK LOGISTIC CONCEPTS LTD.

DATE OF AWARD:

27 - 12 - 2019

CONTRACT SUM:

145,657,098.76

PROJECT IMPACT ASSESSMENT:

THE PROJECT HAS BEEN PUT TO USE



13.05 GEOPOLITICAL ZONE: NORTH WEST

STATE: KANO

LOCAL GOVERNMENT: NASARAWA

PROJECT LOCATION: YANKABA

PROJECT TITLE: PROVISION OF 500KVA TRANSFORMER

STATUS OF PROJECT: COMPLETED

NAME OF CONTRACTOR: SIDI-QUI CONTRACTOR NIG. LTD. LTD.

DATE OF AWARD: 27 - 12 - 2019

CONTRACT SUM: 78,000,000.00

PROJECT IMPACT ASSESSMENT: THE PROJECT HAS BEEN PUT TO USE



13.06 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	KANO
LOCAL GOVERNMENT:	NASARAWA
PROJECT LOCATION:	FEDERAL HOUSING SHARADA
PROJECT TITLE:	PROVISION OF 500KVA TRANSFORMER
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	SIDI-QUI CONTRACTOR NIG. LTD. LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	78,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS BEEN PUT TO USE



**MONITORING/ VERIFICATION OF
CAPITAL PROJECTS IN KADUNA STATE.**

GEO POLITICAL ZONE:	NORTH WEST
STATE:	KADUNA
LGA:	ZARIA LGA KADUNA STATE
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BORE HOLE
PROJECT LOCATION:	PRIMARY HEALTH CARE MAGUME, ZARIA LGA
DATE OF AWARD:	MAY 6 th 2020
PROJECT STATUS:	THE PROJECT IS COMPLETED.
CONTRACT SUM	N 11,666,666.665
NAME OF CONTRACTOR:	MESSRS ACCROM SERVICE NIGERIA LTD
PROJECT IMPACT ASSESSMENT:	THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS ALOT AS THIS IS THE ONLY BOREHOLE IN THE AREA.
LOCAL GOVERNMENT	ZARIA LGA, KADUNA



14.01 GEO POLITICAL ZONE:

NORTH WEST

STATE:

KADUNA

DATE OF AWARD:

MARCH 2nd 2020

CONTRACT SUM

N 11,666,666.00

PROJECT STATUS:

THE PROJECT IS COMPLETED

NAME OF CONTRACTOR:

ELE-CO WORKS LTD

PROJECT IMPACT ASSESSMENT:

THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS A LOT AS THIS IS THE ONLY BOREHOLE IN THE AREA.

LGA:

ZARIA LGA, KADUNA.

PROJECT TITLE:

INSTALLATION OF 500KVA/11/0.415KVA TRANSFORMER

PROJECT LOCATION:

TUDUN WADA, ZARIA LGA



SIGN BOARD



OVERHEAD TANK WITH SOLER PANEL



INDUSTRIAL WATER FILTER


14.02 GEO POLITICAL ZONE:	NORTH WEST
STATE:	KADUNA
DATE OF AWARD:	MAY 6 th 2020
CONTRACT SUM	N 26,000,000.00
PROJECT STATUS:	THE PROJECT IS COMPLETED
NAME OF CONTRACTOR:	MESSRS SIDDI-QUI CONTACTORS LTD
PROJECT IMPACT ASSESSMENT:	THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS A LOT AS THIS IS THE ONLY SOURCE OF POWER IN THE COMMUNITY.
LGA:	ZARIA LGA, KADUNA.
PROJECT TITLE:	INSTALLATION OF 500KVA/11/0.415KVA TRANSFORMER
PRPJECT LOCATION:	SAMARU ZARIA LGA



SIGN BOARD



500 KVA TRANSFORMER

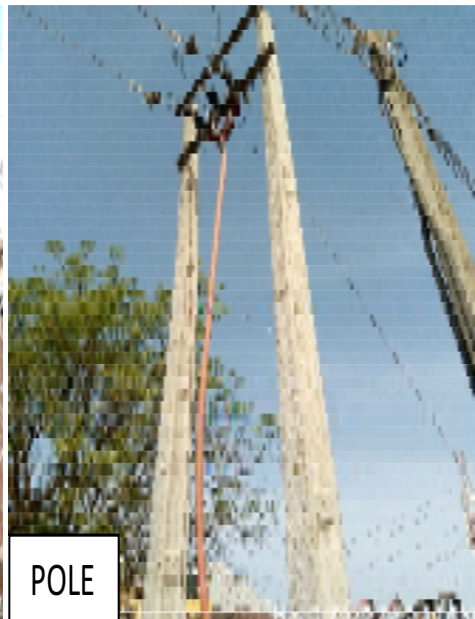

POLE

14.03 GEO POLITICAL ZONE:	NORTH WEST
STATE:	KADUNA
DATE OF AWARD:	MAY 6 th 2020
CONTRACT SUM	N 11,666,666.665
PROJECT STATUS:	THE PROJECT IS COMPLETED
NAME OF CONTRACTOR:	ACCROM SERVICE NIGERIA LTD
PROJECT IMPACT ASSESSMENT:	THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS A LOT AS THIS IS THE ONLY BOREHOLE IN THE AREA.
LGA:	ZARIA LGA, KADUNA
PROJECT TITLE:	INSTALLATION OF 500KVA/11/0.415KVA TRANSFORMER POLE SIGN BOARD 500 KVA TRANSFORMER
PROJECT LOCATION:	MALALI JARKASA, ZARIA LGA



TAP



INDUSTRIAL WATER FILTER



OVRHEAD TANK WITH SOLAR PANEL

**14.04 GEO POLITICAL ZONE:
STATE:**

**NORTH WEST
KADUNA**

DATE OF AWARD:

MAY 6th 2020

CONTRACT SUM

N 26,000,000.00

PROJECT STATUS:

THE PROJECT IS COMPLETED

NAME OF CONTRACTOR:

MESSRS SIDDI-QUI CONTRACTORS LTD

PROJECT IMPACT ASSESSMENT:

THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS A LOT AS THIS IS THE ONLY SOURCE OF POWER IN THE AREA.

LGA:

KADUNA LGA, KADUNA STATE

PROJECT TITLE:

CONSTRUCTION OF SOLAR BOREHOLE

PROJECT LOCATION:

MAHAUTAN KAWO KADUNA NORTH



14.05 GEO POLITICAL ZONE:
STATE:
DATE OF AWARD:

NORTH WEST
KADUNA
MARCH 2nd 2020

CONTRACT SUM

N 11,666,666.00

PROJECT STATUS:

THE PROJECT IS COMPLETED

NAME OF CONTRACTOR:

ECHUS SERVICES LTD

PROJECT IMPACT ASSESSMENT:

THIS PROJECT BENEFIT THE COMMUNITY AND ITS ENVIRONS A LOT AS THIS IS THE ONLY BOREHOLE AND SOURCE OF GOOD WATER IN THE AREA.

PROJECT LOCATION:

KADUNA NORTH, KADUNA STATE



SIGN BOARD



TAP



INDUSTRIAL WATER FILTER

15.0 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

KANKIA

PROJECT LOCATION

FAKUWA

PROJECT TITLE

CONSTRUCTION OF SOLAR BORE HOLE

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

NJEB VENTURES NIG. LTD.

DATE OF AWARD

27th DECEMBER, 2019

PROJECT COST


N11 -666.666.00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE COMMUNITY



15.01 GEO-POLITICAL ZONE	-	NORTH WEST
STATE	-	KATSINA
L.G.A	-	KANKARA
PROJECT LOCATION	-	DANMARKE
PROJECT TITLE	-	CONSTRUCTION OF ROADS
STATUS OF PROJECT	-	100% COMPLETED
NAME OF CONTRACTOR	-	ROCKBOROUGH XI PRIME LTD
DATE OF AWARD	-	27th DECEMBER, 2019.
PROJECT COST	-	N39 9,999,950.00
PROJECT IMPACT ASSESSMENT		THE PROJECT IS IN USE BY THE COMMUNITY !

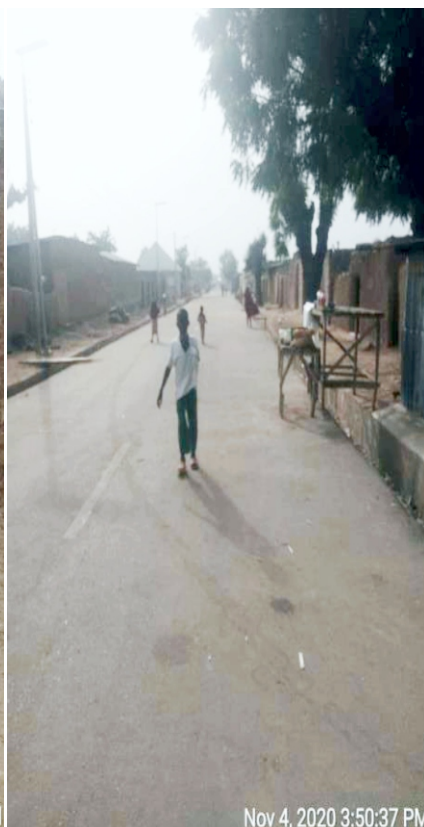

15.02 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

MALUMFASHI

PROJECT LOCATION

MALUMFASHI /KAFUR

PROJECT TITLE

CONSTRUCTION OF DEEPWELL BOREHOLE

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

NORTHON INNOVATION SERVICES LTD.

DATE OF AWARD

27th DECEMBER, 2019.

PROJECT COST

N30,843,878.00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE COMMUNITY!



15.03 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

KANKARA

PROJECT LOCATION

YARGOJE

PROJECT TITLE

CONSTRUCTION AND REHAB. OF ROAD.

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

SHAZ UMA MI NIG. LTD.

DATE OF AWARD

27th DECEMBER, 2019.

PROJECT COST

N299,999,950 .00

**PROJECT IMPACT
ASSESSMENT**

**THE PROJECT IS IN USE BY THE
COMMUNITY!**



15.04 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

KUSADA

PROJECT LOCATION

KANKIA, KUSADA AND INGAWA

PROJECT TITLE

CONSTRUCTION OF SOLAR BORE HOLE

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

EMTAG NIG LTD.

DATE OF AWARD

27th DECEMBER, 2019.

PROJECT COST

N10,804,499.00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE COMMUNITY!



15.05 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

DAUIA

PROJECT LOCATION

COLLEGE OF LEGAL STUDIES

PROJECT TITLE

CONS. REHAB. AND RENOVATION OF SCHOOL.

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

YANDUNA VENTURES LTD.

DATE OF AWARD

27th DECEMBER, 2019.

PROJECT COST

N250,000,000.00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE COMMUNITY!



15.06 GEO-POLITICAL ZONE

NORTH WEST

STATE

KATSINA

L.G.A

KUSADA

PROJECT LOCATION

SABARU

PROJECT TITLE

CONSTRUCTION OF SOLAR BOREHOLE

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

TOWN ONP NIG. LTD.

DATE OF AWARD

27th DECEMBER, 2019.

PROJECT COST

N11 -666.666.00

**PROJECT IMPACT
ASSESSMENT**

**THE PROJECT IS IN USE BY THE
COMMUNITY !**



16.0 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	JIGAWA
LOCAL GOVERNMENT:	TAURA
PROJECT LOCATION:	GOVERNMENT GIRLS SECONDARY SCH.
PROJECT TITLE:	CONSTRUCTION OF SOLAR POWERED BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	CMG PROJECTS LIMITED
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	11,666,666.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



16.01 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	JIGAWA
LOCAL GOVERNMENT:	KAFIN HAUSA LGA
PROJECT LOCATION:	KAFIN HAUSA
PROJECT TITLE:	CONSTRUCTION OF ONE BLOCK OF THREE CLASSROOMS
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	FULUS SYNERGY LIMITED
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	14,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



16.02 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

DAGANA GURI LGA

PROJECT LOCATION:

DAGANA GURI

PROJECT TITLE:

PROVISION OF SOLAR POWER BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

HUX SYNERGY LIMITED

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

34,999,998.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



16.03 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

BALLAMI KAZAURE LGA

PROJECT LOCATION:

BALLAMI KAZAURE

PROJECT TITLE:

PROVISION OF SOLAR POWER BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

HUX SYNERGY LIMITED

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

34,999,998.00

PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING



16.04 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

KAZAURE LGA

PROJECT LOCATION:

KANTI KAZAURE

STATUS OF PROJECT:

COMPLETED

**PROJECT TITLE:
NAME OF CONTRACTOR:**

PROVISION OF SOLAR POWER BOREHOLE

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

**GOLDEN GENERATION GLOBAL GENERATION LIMITED
11,666,666.00**

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



16.05 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	JIGAWA
LOCAL GOVERNMENT:	YANKWASHI LGA
PROJECT LOCATION:	KARKANA
PROJECT TITLE:	PROVISION OF SOLAR POWER BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	MARK & CHAIN VENTURES LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	11,666,666.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



16.06 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

YANKWASHI LGA

PROJECT LOCATION:

KARKANA

PROJECT TITLE:

**PERIMETER FENCING OF KARKANA PRIMARY
HEALTH CARE FACILITY**

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

NAJORI NIGERIA LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

92,610,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS COMPLETED



16.07 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

BABURA LGA

PROJECT LOCATION:

BABURA/GARKI FEDERAL CONSTITUENCY

PROJECT TITLE:

PROVISION OF POWER STREET LIGHTS

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

NAJORI NIGERIA LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

9,250,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



16.08 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

BIRINIWA LGA

PROJECT LOCATION:

DANGISA VILLAGE

PROJECT TITLE:

CONSTRUCTION OF DEEPWELL BOREHOLES

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

BROWN INTEGRATED ENERGY SERVICE LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

80,000,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



16.09 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

JIGAWA

LOCAL GOVERNMENT:

BIRINIWA LGA

PROJECT LOCATION:

DANGISA VILLAGE

PROJECT TITLE:

CONSTRUCTION OF DEEPWELL BOREHOLES

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

BROWN INTEGRATED ENERGY SERVICE LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:


80,000,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



16.10 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	JIGAWA
LOCAL GOVERNMENT:	BIRINIWA LGA
PROJECT LOCATION:	DANGISA VILLAGE
PROJECT TITLE:	CONSTRUCTION OF DEEPWELL BOREHOLES
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	BROWN INTEGRATED ENERGY SERVICE LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	80,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING

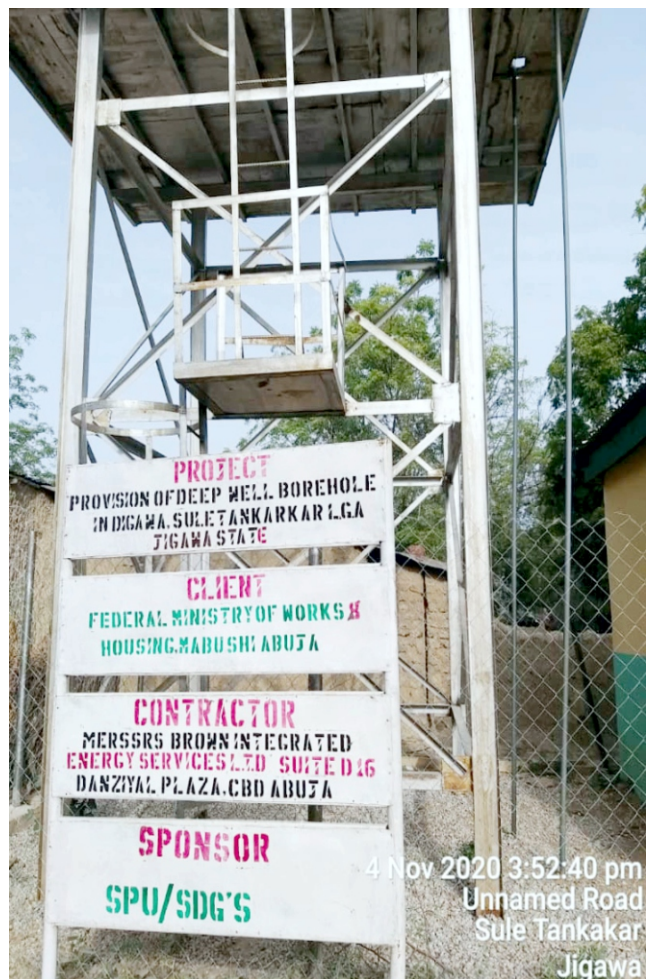

17.0 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	SOKOTO STATE
LOCAL GOVERNMENT:	SOKOTO STATE
PROJECT LOCATION:	SOKOTO STATE
PROJECT TITLE:	CONSTRUCTION OF BLOCK OF 3 CLASSROOM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	HASSONS MULTI RESOURCES LTD
DATE OF AWARD:	2019
CONTRACT SUM:	N12,308,706.03
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



17.01 GEOPOLITICAL ZONE:

NORTH WEST

STATE:

SOKOTO STATE

LOCAL GOVERNMENT:

SOKOTO STATE

PROJECT LOCATION:

SOKOTO STATE

PROJECT TITLE:

PROVISION OF SOLAR POWERED
BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

NEEDS TECHNOLOGIES LTD

DATE OF AWARD:

2019

CONTRACT SUM:

N11,666,666.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



18.0	GEOPOLITICAL ZONE STATE LOCAL GOVERNMENT PROJECT LOCATION PROJECT TITLE STATUS OF PROJECT NAME OF CONTRACTOR DATE OF AWARD CONTRACT SUM (₦) PROJECT IMPACT ASSESSMENT	NORTH-WEST KEBBI BAGUDO LOLO CONSTRUCTION OF 1NO. BLOCK OF 3 CLASSROOMS COMPLETED, IN GOOD CONDITION MESSRS DETASK BUSINESS ENT. LTD. 27/12/2019 14,000,000.00 HIGHLY IMPORTANT, IN GOOD CONDITION, BEING USED BY THE COMMUNITY
-------------	--	---



18.01	GEOPOLITICAL ZONE	NORTHWEST
	STATE	KEBBI
	LOCAL GOVERNMENT	JEGA
	PROJECT LOCATION	OK AREA, JEGA
	PROJECT TITLE	CONSTRUCTION OF A BLOCK OF 2 CLASSROOMS
	STATUS OF PROJECT	COMPLETED, AFFECTED BY FLOODING
	NAME OF CONTRACTOR	MESSRS . TOMLAD NIGERIA LIMITED
	DATE OF AWARD	22 /12/2019
	CONTRACT SUM(₦)	12,965,400.00
	PROJECT IMPACT ASSESSMENT	HIGHLY IMPORTANT , AFFECTED BY FLOODING, BEING USED BY THE COMMUNITY



18.02	GEOPOLITICAL ZONE	NORTH- WEST
	STATE	KEBBI
	LOCAL GOVERNMENT	BIRNIN KEBBI
	PROJECT LOCATION	BEHIND CENTRAL MOSQUE BIRNIN KEBBI
	PROJECT TITLE	SUPPLY AND INSTALLATION OF 1NO. 500KVA TR.
	STATUS OF PROJECT	COMPLETED AND FULLY FUNCTIONING
	NAME OF CONTRACTOR	MESSRS . RISZA GLOBAL SERVICES LTD.
	DATE OF AWARD	27 /12/2019
	CONTRACT SUM(N)	13,000,000.00
	PROJECT IMPACT ASSESSMENT	HIGHLY IMPORTANT , BEING USED BY THE COMMUNITY



18.03	GEOPOLITICAL ZONE	NORTH WEST
	STATE	KEBBI
	LOCAL GOVERNMENT	JEGA
	PROJECT LOCATION	UNGUWAR DUTSIN ZAGI, JEGA
	PROJECT TITLE	CONSTRUCTION OF 1NO. BLOCK OF 2 CLASSROOMS
	STATUS OF PROJECT	COMPLETED AND FULLY FUNCTIONING
	NAME OF CONTRACTOR	MESSRS COULDRON NIGERIA LIMITED
	DATE OF AWARD	27 /12/2019
	CONTRACT SUM (₦)	12,965,400.00
	PROJECT IMPACT ASSESSMENT	HIGHLY IMPORTANT , BEING USED BY THE COMMUNITY



18.04	GEOPOLITICAL ZONE	NORTHWEST
	STATE	KEBBI
	LOCAL GOVERNMENT	BAGUDO
	PROJECT LOCATION	LOLO TOWN
	PROJECT TITLE	SUPPLY AND INSTALLATION OF SOLAR BOREHOLE
	STATUS OF PROJECT	COMPLETED AND FULLY FUNCTIONING
	NAME OF CONTRACTOR	MESSRS. DETASK BUSINESS ENTERPRISES LTD.
	DATE OF AWARD	27 /12/2019
	CONTRACT SUM (₦)	11,666,666.00
	PROJECT IMPACT ASSESSMENT	HIGHLY IMPORTANT, BEING USED BY THE COMMUNITY



**18.05 GEOPOLITICAL ZONE
STATE**

LOCAL GOVERNMENT

PROJECT LOCATION

PROJECT TITLE

STATUS OF PROJECT

NAME OF CONTRACTOR

DATE OF AWARD

CONTRACT SUM (₦)

PROJECT IMPACT

ASSESSMENT

NORTHWEST

KEBBI

KALGO, ALIERO

KALGO TOWN, ALIERO TOWN

PROVISION OF 200 NOS INTEGRATED SOLAR STREET LIGHTS
IN KEBBI CENTRAL SENATORIAL DISTRICT

COMPLETED AND FULLY FUNCTIONING

MESSRS. VIANY GLOBAL INVESTMENT LTD.

27 /12/2019

220,000,000.00

HIGHLY IMPORTANT , BEING USED BY THE
COMMUNITY



18.06	GEOPOLITICAL ZONE	NORTHWEST
	STATE	KEBBI
	LOCAL GOVERNMENT	ARGUNGU, AUGIE
	PROJECT LOCATION	PALACE AREA, ARGUNGU, AUGIE TOWN
	PROJECT TITLE	PROVISION OF 227 NOS INTEGRATED SOLAR STREET LIGHTS IN KEBBI NORTH SENATORIAL DISTRICT
	STATUS OF PROJECT	COMPLETED AND FULLY FUNCTIONING
	NAME OF CONTRACTOR	MESSRS CRUISE SRS TRADING NIG. LTD.
	DATE OF AWARD	27 /12/2019
	CONTRACT SUM (₦)	249,700,000.00
	PROJECT IMPACT ASSESSMENT	HIGHLY IMPORTANT , BEING USED BY THE COMMUNITY



Nov 18, 2020 4:31:00 PM



Nov 18, 2020 5:03:41 PM

19.0 GEOPOLITICAL ZONE:	NORTH WEST
STATE:	ZAMFARA
LOCAL GOVERNMENT:	GUSAU
PROJECT LOCATION:	GUSAU ZAMFARA
PROJECT TITLE:	CONSTRUCTION OF FED. SEC. OFFICE COMPLEX
STATUS OF PROJECT:	85%
NAME OF CONTRACTOR:	M/S SAGETO LTD
DATE OF AWARD:	2011
CONTRACT SUM:	N2,619,168,176.77
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS ABOUT TO BE USE



20.0	GEO-POLITICAL ZONE:	SOUTH EAST
	STATE:	IMO
	CONTRACTOR:	M/S AE & E LTD.
	PROJECT TITLE:	CONSTRUCTION OF ROADS, DRAINS AND
	PROJECT LOCATION:	IHIALA ORLU, UMUDURU EXPRESS WAY SPUR TO OHIARA RIVER BRIDGE IHITENANSA ORSU, IMO STATE.
	DATE OF AWARD:	27TH DECEMBER, 2019.
	AMOUNT:	148,765,213.01
	PERCENTAGE COMPLETION :	70%
	IMPACT ASSESSMENT :	THE WORK IS AT 70% COMPLETION AS THE DRAINAGE WORKS IS ALREADY COMPLETED AND THE FILLING OF THE ROAD AT A TOP STAGE.



20.01 GEO-POLITICAL ZONE:

SOUTH EAST

STATE:

IMO

CONTRACTOR :

M/S DIGITAL GEOSPATIAL TECHNOLOGY SOLUTION LTD.

PROJECT TITLE:

SUPPLY AND INSTALLATION OF 500KVA TRANSFORMER.

LOCATION:

OKAI VILLAGE EZIANA TOWN, ISIALA MBANO L.G.A

DATE OF AWARD:

27TH DECEMBER, 2019.

AMOUNT:

26,000,000.00

PERCENTAGE COMPLETION:

100%

IMPACT ASSESSMENT :

THE PROJECT IS COMPLETED BUT NOT COMMISSIONED AS NEMSAHAS REFUSED TO GIVE APPROVAL FOR THE COMMISSIONING AND CONNECTION OF THE TRANSFORMER TO THE 33KVA HIGH TENSION TILL DATE .



20.02 GEO-POLITICAL ZONE: SOUTH EAST

STATE: IMO

CONTRACTOR: CENTER VIEW BUSINESS CONCEPT LTD.

PROJECT TITLE: CONSTRUCTION OF A BLOCK OF CLASSROOM

PROJECT LOCATION: IGWEBUIKE PRIMARY SCHOOL, IBEME ISIALA MBANO
L.G.A IMO SENATORIAL DISTRICT.

DATE OF AWARD: AMOUNT: 18,522,000.00

PERCENTAGE COMPLETION: 100%

IMPACT ASSESSMENT: THE PROJECT IS COMPLETED AND STUDENTS STAFF
OF THE SCHOOL ARE MAKING GOOD USE OF IT AND
THANKFUL TO THE FEDERAL GOVERNMENT.



20.03 GEO-POLITICAL ZONE: SOUTH EAST

STATE: IMO

CONTRACTOR: M/S LEMMYFAITH & PARTNER LTD.

PROJECT TITLE: REHABILITATION OF CLASSROOM BLOCK

PROJECT LOCATION: IGWE BUIKE PRIMARY SCHOOL,
IBEME ISIALA MBANO L.G.A IMO SENATORIAL
DISTRICT.

DATE OF AWARD:

AMOUNT: 18,522,000.00

PERCENTAGE COMPLETION: 100%

IMPACT ASSESSMENT: THE PROJECT IS COMPLETED BOTH THE
STUDENTS AND THE STAFF ARE MAKING GOOD
USE OF THE FACILITY AND THANKFUL TO THE
FEDERAL GOVERNMENT.



20.04 GEO-POLITICAL ZONE:	SOUTH EAST
STATE:	IMO
CONTRACTOR:	M/S DEFENSIVE & PROTECTIVE CONCEPT LTD.
PROJECT TITLE:	CONSTRUCTION OF MOTORIZED BOREHOLE
LOCATION:	EHIME MBANO L.G.A. IMO STATE
DATE OF AWARD:	27TH DECEMBER,2019.
AMOUNT:	72,000,000.00
PERCENTAGE COMPLETION:	100%
IMPACT ASSESSMENT :	PROJECT FAILED.



20.05 GEO-POLITICAL ZONE:	SOUTH EAST
STATE:	IMO
CONTRACTOR:	M/S DEFENSIVE & PROTECTIVE CONCEPT LTD.
PROJECT TITLE:	CONSTRUCTION OF MOTORIZED BOREHOLE
LOCATION:	EHIME MBANO L.G.A. IMO STATE
DATE OF AWARD:	27TH DECEMBER,2019.
AMOUNT:	72,000,000.00
PERCENTAGE COMPLETION:	100%
IMPACT ASSESSMENT :	THE PROJECT IS COMPLETE AND FUNCTIONING



20.06 GEO-POLITICAL ZONE: SOUTH EAST

STATE: IMO

CONTRACTOR: INNOCADAND WAVES WIG LTD.

PROJECT TITLE: CONSTRUCTION OF SOLAR POWERED BOREHOLES

LOCATION: UMUEZIE NGURU, AGOHIMO MBAISE

DATE OF AWARD: 27THDECEMBER,2019.

AMOUNT: 23,333,333.00

PERCENTAGE COMPLETION: 100%

IMPACT ASSESSMENT: THE PROJECT IS COMPLETED AND FUNCTIONING
THE RESIDENTS AND VILLAGERS ARE MAKING GOOD
USE OF THE BOREHOLE.



20.07 GEO-POLITICAL ZONE: SOUTH EAST

STATE: IMO

CONTRACTOR: M/S DEFENSIVE & PROTECTIVE CONCEPT LTD.

PROJECT TITLE: CONSTRUCTION OF MOTORIZED BOREHOLE

LOCATION: EHIME MBANO L.G.A. IMO STATE

DATE OF AWARD: 27TH DECEMBER, 2019.

AMOUNT: 72,000,000.00

PERCENTAGE COMPLETION: 100%

IMPACT ASSESSMENT : THE PROJECT IS COMPLETED AND FUNCTIONING.



21.0 GEO-POLITICAL ZONE: SOUTH EAST

STATE: ENUGU

LOCAL GOVERNMENT: ENUGU SOUTH

PROJECT LOCATION: FED. GOVT. SITE AND SREVICES SCHEME, REPUBLIC LAYOUT, ENUGU

PROJECT TITLE: PROVISION OF INFRASTRUCTURES (WATER) SPECIAL INTERVENTION

STATUS OF PROJECT: COMPLETED

NAME OF CONTRACTOR: M/S FULA REAL ESTATE LTD.

DATE OF AWARD: 27 - 12 - 2019

CONTRACT SUM: 40,731,608.57

PROJECT IMPACT ASSESSMENT: THE PROJECT IS NOT FUNCTIONING



21.01 GEO-POLITICAL ZONE:

SOUTH EAST

STATE:

ENUGU

LOCAL GOVERNMENT:

AWGU

PROJECT LOCATION:

GENERAL HOSPITAL, AWGU TOWN

PROJECT TITLE:

PROVISION AND INSTALLATION OF
TRANSFORMER AND SOLAR STREET LIGHT

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

NANIC INVESTMENT SERVICE LTD.

DATE OF AWARD:

27 - 12 - 2019

CONTRACT SUM:

68,880,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



22.0 GEO-POLITICAL ZONE: SOUTH EAST
STATE: EBONYI STATE
PROJECT TITLE: CONSTRUCTION OF SOLAR POWERED BOREHOLE
PROJECT LOCATION: EKKA COMMUNITY EZZA NORTH LGA
NAME OF CONTRACTOR: PAZINO ENGINEERING AND CONSTRUCTION CO. LIMITED
DATE OF AWARD: 19TH DECEMBER, 2019
LGA:
STATUS OF PROJECT: COMPLETED
CONTRACT SUM: N11,666,666.00
PROJECT IMPACT ASSESSMENT: PROVIDE PORTABLE WATER FOR THE COMMUNITY, REDUCE WATER BORE DISEASE



22.01 GEO-POLITICAL ZONE:

SOUTH EAST

STATE:

EBONYI STATE

PROJECT TITLE:

CONSTRUCTION OF DEEPWALL BOREHOLE
EKKA COMMUNITY NORTH EBONYI (ALEX
EKWUEME TEACHING HOSPITAL)

PROJECT LOCATION:

NAME OF CONTRACTOR:

SYSESCENT GLOBAL SERVICES LIMITED

DATE OF AWARD:

19TH DECEMBER, 2019

LGA:

STATUS OF PROJECT:

COMPLETED

CONTRACT SUM:


FIVE (5) PROJECTS TOTALING N82,950,000.00

PROJECT IMPACT ASSESSMENT:

PROVIDE PORTABLE WATER FOR THE COMMUNITY,
REDUCE WATER BORE DISEASE



22.02 GEO-POLITICAL ZONE:	SOUTH EAST
STATE:	EBONYI STATE
PROJECT TITLE:	CONSTRUCTION OF DEEPWALL BOREHOLE
PROJECT LOCATION:	EZI-AKANI UKPA COMMUNITY, AFIKPO
NAME OF CONTRACTOR:	SYSESCENT GLOBAL SERVICES LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
LGA:	
STATUS OF PROJECT:	COMPLETED
CONTRACT SUM:	FIVE (5) PROJECTS TOTALING 82,950,000.00
PROJECT IMPACT ASSESSMENT:	PROVIDE PORTABLE WATER FOR THE COMMUNITY, REDUCE WATER BORE DISEASE

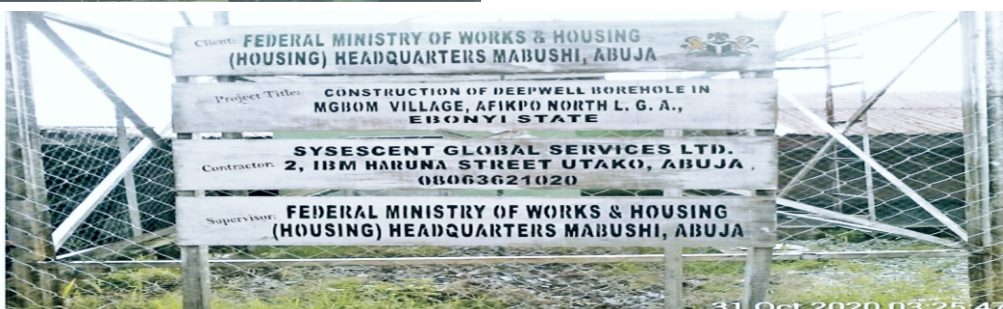

22.03 GEO-POLITICAL ZONE:	SOUTH EAST
STATE:	EBONYI STATE
PROJECT TITLE:	CONSTRUCTION OF DEEPWALL BOREHOLE
PROJECT LOCATION:	AMAIZU VILLAGE, AFIKKPO
NAME OF CONTRACTOR:	SYSESCENT GLOBAL SERVICES LIMITED
DATE OF AWARD:	19TH DECEMBER, 2019
LGA:	
STATUS OF PROJECT:	COMPLETED
CONTRACT SUM:	FIVE (5) PROJECTS TOTALING 82,950,000.00
PROJECT IMPACT PROVIDE :	PORTABLE WATER FOR THE COMMUNITY, REDUCE WATER BORE DISEASE, ETC



22.04 GEO-POLITICAL ZONE:

SOUTH EAST

STATE:

EBONYI STATE

PROJECT TITLE:

CONSTRUCTION OF DEEPWALL BOREHOLE

PROJECT LOCATION:

IBAGWO-EKKA COMMUNITY, AFIKPO

NAME OF CONTRACTOR:

SYSESCENT GLOBAL SERVICES LIMITED

DATE OF AWARD:

19TH DECEMBER, 2019

LGA:

STATUS OF PROJECT:


COMPLETED

CONTRACT SUM:

FIVE (5) PROJECTS TOTALING N82,950,000.00

PROJECT IMPACT ASSESSMENT:

**PROVIDE PORTABLE WATER FOR THE COMMUNITY,
REDUCE WATER BORE DISEASE**

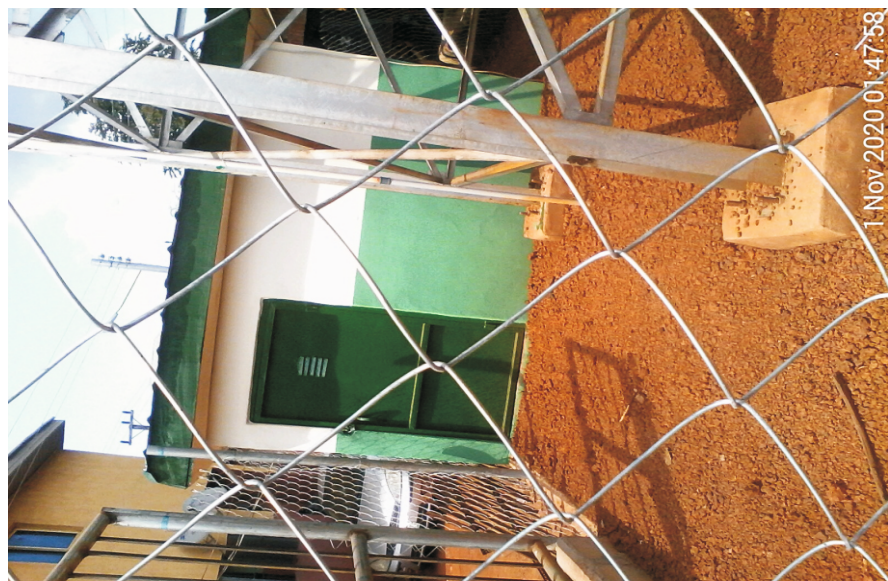

23.0 GEOPOLITICAL ZONE:	SOUTH EAST
STATE:	ABIA
LOCAL GOVERNMENT:	BENDE, ISIKWUATOR & OHAOFIA
PROJECT LOCATION:	BENDE, ISIKWUATOR & OHAOFIA
PROJECT TITLE:	SUPPLY AND INSTALLATION OF SOLAR STREET LIGHT
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	CATCHMATE VENTURES LTD.
DATE OF AWARD:	24 - 05 - 2019
CONTRACT SUM:	385,965,461.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



Nov 3, 2020 4:01:58 PM



Nov 3, 2020 4:03:00 PM



Nov 2, 2020 12:07:43 PM



Nov 2, 2020 3:15:18 PM

23.01 GEOPOLITICAL ZONE:	SOUTH EAST
STATE:	ABIA
LOCAL GOVERNMENT:	OZARTA VILLAGE, UKWA WEST LGA
PROJECT LOCATION:	OZARTA VILLAGE
PROJECT TITLE:	CONSTRUCTION OF DEEPWELL BOREHOLES
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	NORTON INNOVATIONS SERVICES LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	36,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



23.02 GEOPOLITICAL ZONE:	SOUTH EAST
STATE:	ABIA
LOCAL GOVERNMENT:	UKWA EAST LGA
PROJECT LOCATION:	CENTRAL PRIMARY SCHOOL, OBIOHIA
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 3 CLASS ROOM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	JAMOKWET INVESTMENT LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	14,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



23.03 GEOPOLITICAL ZONE:

SOUTH EAST

STATE:

ABIA

LOCAL GOVERNMENT:

UMUAHIA SOUTH LGA

PROJECT LOCATION:

AMANKWO VILLAGE

PROJECT TITLE:

CONSTRUCTION OF SOLAR POWERED BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

SGOCH NETWORK LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

11,666,666.00

PROJECT IMPACT ASSESSMENT: THE PROJECT IS FUNCTIONING



23.04 GEOPOLITICAL ZONE:

SOUTH EAST

STATE:

ABIA

LOCAL GOVERNMENT:

OHUHU-UMUAHIA NORTH LGA

PROJECT LOCATION:

UMKABIA OKAIUGA ALIKE AUTONOMOUS COMM.

PROJECT TITLE:

CONSTRUCTION OF SOLAR POWERED BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

MAKSYLVE INTERNATIONAL LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

11,666,666.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



23.05 GEOPOLITICAL ZONE:	SOUTH EAST
STATE:	ABIA
LOCAL GOVERNMENT:	BENDE LGA
PROJECT LOCATION:	BENDE FEDERAL CONSTITUENCY
PROJECT TITLE:	CONSTRUCTION OF MATERNITY HEALTH CENTRE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	J. BANDE B. SYLMAR LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	14,065,122.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



23.06 GEOPOLITICAL ZONE:

SOUTH EAST

STATE:

ABIA

LOCAL GOVERNMENT:

OLOKORO SOUTH LGA

PROJECT LOCATION:

UMUNTU VILLAGE

PROJECT TITLE:

CONSTRUCTION OF SOLAR STREET LIGHT

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

FIRST PRICELESS INTEGRATED INVESTMENT LTD.

DATE OF AWARD:

19 - 12 - 2019

CONTRACT SUM:

44,701,213.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



24.0 GEO-POLITICAL ZONE:	SOUTH WEST
STATE:	OYO
LGA:	IBADAN
PROJECT LOCATION:	OYO STATE FIELD OFFICE
PROJECT TITLE:	REPLACEMENT OF 2 NO. 500KVA DISTRIBUTION TRANSFORMERS
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	ALH AUDU DYNAMIC NIGERIA LIMITED
DATE OF AWARD:	
CONTRACT SUM:	N20, 475,000.00
PROJECT IMPACT ASSESMENT:	IMPROVED SECURITY OF LIVES AND PROPERTIES



24.01 GEO-POLITICAL ZONE: SOUTH WEST

STATE: OYO

LGA: IBADAN

PROJECT LOCATION: FIDITI LINKAGE ROAD TO THE EXPRESS

PROJECT TITLE: CONSTRUCTION OF DRAINAGE AND CULVERT

STATUS OF PROJECT: COMPLETED (100%)

NAME OF CONTRACTOR: TCG NIGERIA LIMITED

DATE OF AWARD: 14-03-2019

CONTRACT SUM: N60, 000,000.00

PROJECT IMPACT ASSESMENT: CREATING OF FREE FLOW WATER WAYS



24.02 GEO-POLITICAL ZONE:	SOUTH WEST
STATE:	OYO
LGA:	AFIJO
PROJECT LOCATION:	METHODIST SECONDARY SCHOOL IWARE OYO
PROJECT TITLE:	CONSTRUCTION OF 3 CLASSROOMS
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	TRANS-SAHEL ENTERPRISE LIMITED
DATE OF AWARD:	19-12-2019
CONTRACT SUM:	N14, 000,000.00
PROJECT IMPACT ASSESMENT:	(IN USE) IMPROVED EDUCATIONAL ENVIRONMENT



24.03 GEO-POLITICAL ZONE:

SOUTH WEST

STATE:

OYO

LGA:

OGOBOMOSHO

PROJECT LOCATION:

**ANGLICAN GRAMMER SCHOOL SABO
OGBOMOSHO**

PROJECT TITLE:

**REHABILITATION OF ANGLICAN GRAMMAR
SCHOOL HALL OYO**

STATUS OF PROJECT:

COMPLETED (100%)

NAME OF CONTRACTOR:

PRIME TAAD NIGERIA LIMITED

DATE OF AWARD:

19-12-2019

CONTRACT SUM:

N28, 000,000.00

PROJECT IMPACT ASSESSMENT:



24.04 GEO-POLITICAL ZONE: SOUTH WEST

STATE: OYO

LGA: OYO

PROJECT LOCATION: FEDERAL SCHOOL OF SURVEY, MOBOLAJE AYOUT, ISHEKE ^ AWUMORO OYO

PROJECT TITLE: PROVISION OF SOLAR POWERED BOREHOLE

PROJECT STATUS: COMPLETED (100%)

NAME OF CONTRACTOR: ESTIVUS NIGERIA LIMITED

DATE OF AWARD: APRIL 2019

CONTRACT SUM: N58, 333,333.00

PROJECT IMPACT ASSESMENT: IMPROVE SUPPLY OF PORTABLE WATER



24.05 GEO-POLITICAL ZONE: SOUTH WEST

STATE: OYO

LGA: ALAGBON

PROJECT LOCATION: A.U. D PRIMARY SCHOOL ALAGBON

PROJECT TITLE: CONSTRUCTION OF A BLOCK OF 3 CLASS ROOM

STATUS OF PROJECT: COMPLETED (100%)

NAME OF CONTRACTOR: ACHIM INTEGRATED OIL SERVICE AND GAS LIMITED

DATE OF AWARD: 19-12-2019

CONTRACT SUM: N12, 965,400.00

PROJECT IMPACT ASSESMENT: CONDUCIVE ENVIRONMENT FOR LEARINING



25.0	GEOPOLITICAL ZONE:	SOUTH WEST
	STATE:	OGUN STATE
	LGA:	OTA
	PROJECT LOCATION:	ABULE IROKO COMMUNITY OTA
	PROJECT TITLE:	PROVISION OF MOTORIZED BORE HOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	EZIONYE ENTERPRISES NIG. LTD
	DATE OF AWARD:	27TH DECEMBER, 2019
	CONTRACT SUM:	N11,000, 000.00
	PROJECT IMPACT ASSESSMENT:	PRESENTLY IN USE BY THE COMMUNITY



25.01	GEOPOLITICAL ZONE:	SOUTH WEST
	STATE:	OGUN STATE
	LGA:	OTA
	PROJECT LOCATION:	ABULE IROKO COMMUNITY OTA
	PROJECT TITLE:	PROVISION OF MOTORIZED BORE HOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	EZIONYE ENTERPRISES NIG. LTD
	DATE OF AWARD:	N11,000, 000.00
	PROJECT IMPACT ASSESSMENT:	INSTEAD OF COMPLETE REPLACEMENT OF THE FACILITY, IT WAS IMPROVED AND MAINTAINED. SECONDLY, THE FACILITY IS DISCONNECTED FROM THE NATIONAL GRID BECAUSE THE OFFICE OWED PHCN.



25.02 GEOPOLITICAL ZONE

SOUTH WEST

STATE

OGUN STATE

LGA

OTA

PROJECT LOCATION

ADO ODO

PROJECT TITLE

CONST. OF BLOCK F 3 CLASSROOMS

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

STRUCTURES IN MOTION

DATE OF AWARD


27TH DECEMBER, 2019

CONTRACT SUM

N 28, 000, 000. 00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE
COMMUNITY

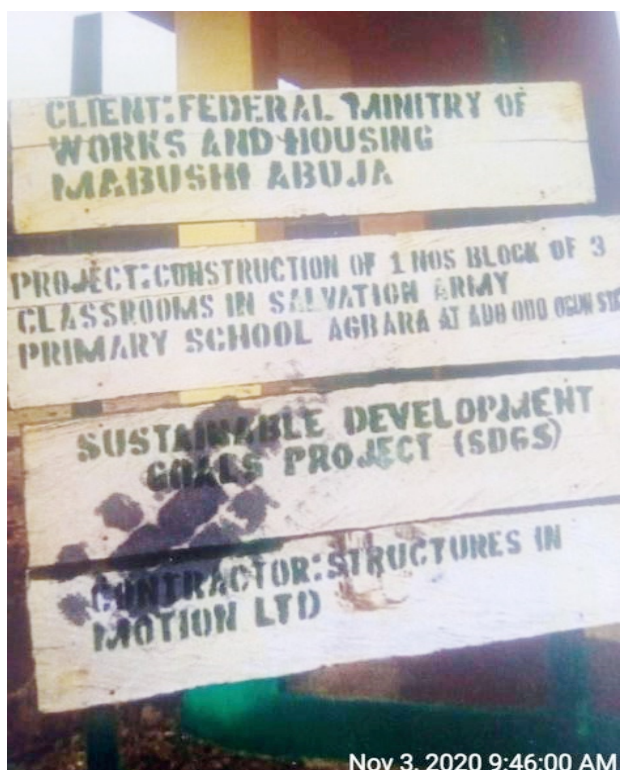

25.03 GEOPOLITICAL ZONE

STATE

LGA

PROJECT LOCATION

PROJECT TITLE

STATUS OF PROJECT

NAME OF CONTRACTOR

DATE OF AWARD

CONTRACT SUM

PROJECT IMPACT ASSESSMENT

SOUTH WEST

OGUN STATE

OTA

FIELD OFFICE ABEOKUTA

CONST. OF DEEPWELL BORE HOLES

100% COMPLETED

OVERZOOM GLOBAL INVEST. SERVICES

27TH DECEMBER, 2019

N 83,000,100,000.00

**THE PROJECT IS IN USE BY THE
COMMUNITY**



25.04 GEOPOLITICAL ZONE

SOUTH WEST

STATE

OGUN STATE

LGA

IPOKIA

PROJECT LOCATION

METHODIST SCHOOL VAWHE HUNDO

PROJECT TITLE

CONST. OF MOTORIZED BORE HOLE

STATUS OF PROJECT

100% COMPLETED

NAME OF CONTRACTOR

NET-TRIK SOLUTIONS LTD

DATE OF AWARD

27TH DECEMBER, 2019

CONTRACT SUM


N 11,000,000.00

PROJECT IMPACT ASSESSMENT

THE PROJECT IS IN USE BY THE
COMMUNITY



25.05	GEOPOLITICAL ZONE	SOUTH WEST
	STATE	OGUN STATE
	LGA	IJEBU-ODE
	PROJECT LOCATION	IMEPE ONDO BENIN ROAD
	PROJECT TITLE	CONST.OF BLOCK OF 3 CLASSROOMS WITH VIP TOILET
	STATUS OF PROJECT	100% COMPLETED
	NAME OF CONTRACTOR	TOMLAD NIG. LTD
	DATE OF AWARD	27TH DECEMBER, 2019
	CONTRACT SUM	N 15,280,650
	PROJECT IMPACT ASSESSMENT	THE PROJECT IS IN USE BY THE

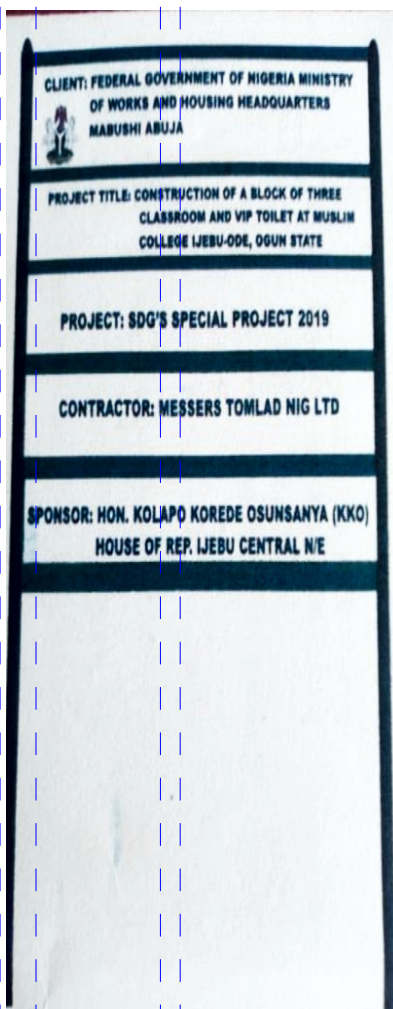

26.0	GEO-POLITICAL ZONE:	SOUTH WEST
	STATE:	OSUN
	LGA:	OSOGBO
	PROJECT LOCATION:	WORU STREET AGUNBELEWO OSOGBO
	PROJECT TITLE:	PROVISION AND INSTALLATION 10POLES ALL IN ONE SOLAR STREET LIGHTING
	STATUS OF PROJECT:	COMPLETED (100%)
	NAME OF CONTRACTOR:	DAKEEM MULTI RESOURCES LIMITED
	DATE OF AWARD:	27-12-2019
	CONTRACT SUM:	N9, 250,000.00
	PROJECT IMPACT ASSESSMENT:	(IN USE) IMPROVED SECURITY OF LIVES AND PROPERTIES



26.01 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

OSOGBO

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESMENT:

SOUTH WEST

OSUN

OSOGBO

ALONG OSOGBO-IBOKUN ROAD OKE-BALE

CONSTRUCTION OF FEDERAL SECRETARIAT COMPLEX

(65%)

GOLDEN NIGERIA LIMITED

20-02-2012

N2, 548, 444,283.00



Nov 3, 2020 5:58:06 PM
Igede - Awo Road
Osogbo
Osun



Nov 3, 2020 5:51:54 PM
Igede - Awo Road
Osogbo
Osun



Nov 3, 2020 5:47:15 PM
Igede - Awo Road
Osogbo
Osun



Nov 3, 2020 5:47:05 PM
Igede - Awo Road
Osogbo
Osun

26.02 GEO-POLITICAL ZONE:	SOUTH WEST
STATE:	OSUN
LGA:	EDE
PROJECT LOCATION:	MUSLIM GRAMMER SCHOOL EDE
PROJECT TITLE:	CONSTRUCTION OF MOTORIZED BOREHOLE
STATUS OF PROJECT:	COMPLETED (100%)
NAME OF CONTRACTOR:	POSITIVE GOALS ACHIEVEMENT NIGERIA LIMITED
DATE OF AWARD:	27-12-2019
CONTRACT SUM:	N11, 000,000.00
PROJECT IMPACT ASSESMENT:	(IN USE) IMPROVED SUPPLY AND QUALITY OF PORTABLE WATER



Nov 4, 2020 11:49:48 AM



Nov 4, 2020 11:48:47 AM
Ede - Abeere Road
Nijhof Advies
Ede North
Osun



Nov 4, 2020 11:49:02 AM
Ede - Abeere Road
Nijhof Advies
Ede North
Osun

27.0	GEO-POLITICAL ZONE:	SOUTH-WEST
	STATE:	LAGOS
	LGA:	ETI-OSA
	PROJECT LOCATION:	RESETTLEMENT CENTRE
	PROJECT TITLE:	PROVISION OF MOTORIZED BOREHOLE
	STATUS OF PROJECT:	100%
	NAME OF CONTRACTOR: 	M/S G-ONE ENERGY LTD.
	DATE OF AWARD:	27TH DECEMBER, 2019
	AMOUNT:	N11, 000,000.00
	PROJECT IMPACT ASSESSMENT:	IMPROVED SUPPLY OF POTABLE WATER



27.01 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

AMOUNT:

PROJECT IMPACT ASSESSMENT:

SOUTH-WEST

LAGOS

(BARIGA)

EVA ADELAJA GIRLS SECONDARY SCHOOL,
BARIGA

PROVISION OF MOTORIZED BOREHOLE

100%

M/S TEL-TWINE NETWORKS LTD.

N11, 000,000.00

IMPROVED SUPPLY OF POTABLE WATER



27.02 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

AMOUNT:

PROJECT IMPACT ASSESSMENT:

SOUTH-WEST

LAGOS

SURULERE

IREPODUN STREET, IJESHATEDO

**CONSTRUCTION AND REHABILITATION OF
ROADS, CULVERTS AND DRAINAGE**

100%

M/S HANABELLA NIG. LTD.

6TH MAY, 2019

N75, 000,000.00

**EASE OF MOVEMENT OF PEOPLE AND
GOODS IN THE AREA**



27.04 GEO-POLITICAL ZONE:

SOUTH-WEST

STATE:

LAGOS

LGA:

IKORODU

PROJECT LOCATION:

IGBOGBO

PROJECT TITLE:

CONSTRUCTION OF MATERNITY HEALTH CENTRE

STATUS OF PROJECT:

100%

NAME OF CONTRACTOR:

M/S EL-TORO NIG.ENTREPRISES.

DATE OF AWARD:

AMOUNT:

N15, 187,476.00

PROJECT IMPACT ASSESSMENT:

TO IMPROVE ACCESS TO QUALITY HEALTH SERVICES



27.03	GEO-POLITICAL ZONE:	SOUTH-WEST
	STATE:	LAGOS
	LGA:	IKORODU
	PROJECT LOCATION:	IBESHE
	PROJECT TITLE:	PROVISION OF MOTORIZED BOREHOLE
	STATUS OF PROJECT:	100%
	NAME OF CONTRACTOR:	M/S SLEEK HILLS NIG. LTD.
	DATE OF AWARD:	
	AMOUNT:	N23, 000,000.00 (COMBINED WITH BLOCK OF CLASSROOMS)
	PROJECT IMPACT ASSESSMENT:	TO IMPROVE THE QUALITY OF POTABLE WATER



27.05 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

AMOUNT:

PROJECT IMPACT ASSESSMENT:

SOUTH-WEST

LAGOS

SURU LERE

LOCAL AUTHORITY (L.A) PRIMARY SCHOOL, ORILE IGANMU

CONSTRUCTION OF 2 BLOCKS OF CLASSROOMS

50%

M/S FAITH UNIVERSAL NIG. LTD.

6TH MAY, 2019

N140,000,000.00 (FOR TEN -10 – BLOCKS OF CLASSROOMS)



27.06 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

AMOUNT:

PROJECT IMPACT ASSESSMENT:

SOUTH-WEST

LAGOS

SURULERE

**CANAL NURSERY/ PRIMARY SCHOOL,
ORILE IGANMU**

**CONSTRUCTION OF BLOCK OF
CLASSROOMS**

50%

M/S FAITH UNIVERSAL NIG. LTD.

6TH MAY, 2019



27.07 GEO-POLITICAL ZONE:

SOUTH-WEST

STATE:

LAGOS

LGA:

SURULERE

PROJECT LOCATION:

AIYETORO PRIMARY SCHOOL, AGUDA

PROJECT TITLE:

CONSTRUCTION OF 2 BLOCKS OF CLASSROOMS

STATUS OF PROJECT:

50%

NAME OF CONTRACTOR:

M/S FAITH UNIVERSAL NIG. LTD.

DATE OF AWARD:

6TH MAY, 2019

AMOUNT:

PROJECT IMPACT ASSESSMENT:



27.08 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

AMOUNT:

PROJECT IMPACT ASSESSMENT:

REMARKS:

SOUTH-WEST

LAGOS

AGUNTASHOLO PRIMARY SCHOOL,
IJESHATEDO

CONSTRUCTION OF 2 BLOCKS OF
CLASSROOMS

20% (SLAB LEVELS)

M/S FAITH UNIVERSAL NIG. LTD.

6TH MAY, 2019

**ORIGINAL LOCATION WAS AT JINADU
BUT FOR LACK OF SPACE IT WAS
TAKEN TO AGUNTASHOLO PRIMARY
SCHOOL, IJESHATEDO.**



27.09 GEO-POLITICAL ZONE:

SOUTH-WEST

STATE:

LAGOS

LGA:

PROJECT LOCATION:

ODOLOWU PRIMARY SCHOOL,
IJESHATEDO

PROJECT TITLE:

CONSTRUCTION OF 2 BLOCKS OF
CLASSROOMS

STATUS OF PROJECT:

50%

NAME OF CONTRACTOR:

M/S FAITH UNIVERSAL NIG. LTD.

DATE OF AWARD:

6TH MAY, 2019

AMOUNT:

PROJECT IMPACT ASSESSMENT:



02/11/2020 02:32 PM

28.0 GEO-POLITICAL ZONE: SOUTH WEST
STATE: EKITI
LGA: EKITI SOUTH WEST
PROJECT LOCATION: COLLEGE OF EDUCATION IKERE AND
 NYSC ORIENTATION CAMP ISE, EKITI SOUTH WEST
 LGA.
PROJECT TITLE: PROVISION OF SOLAR STREET LIGHT.
STATUS OF PROJECT: COMPLETED (100%)
NAME OF CONTRACTOR: TOMLAD NIGERIA LTD.
DATE OF AWARD: 22-12-2019
CONTRACT SUM: ₦23, 034,330.00
PROJECT IMPACT ASSESMENT:



28.01 GEO-POLITICAL ZONE:

SOUTH WEST

STATE:

EKITI

LGA:

ADO EKITI

PROJECT LOCATION:

NEW IYIN ROAD ADO EKITI.

PROJECT TITLE:

CONSTRUCTION OF FEDERAL SECRETARIAT COMPLEX.

STATUS OF PROJECT:

(40%)

NAME OF CONTRACTOR:

DEUX PROJECT LTD.

DATE OF AWARD:

APRIL 2017

CONTRACT SUM:

₦3,340,608,368.07

PROJECT IMPACTASSESSMENT:



28.02

GEO-POLITICAL ZONE:

SOUTH WEST

STATE:

EKITI

LGA:

EYIO EKITI

PROJECT LOCATION:

ST PAUL PRIMARY SCHOOL, EYIO EKITI

PROJECT TITLE:

CONSTRUCTION OF A BLOCK OF CLASSROOMS

STATUS OF PROJECT:

COMPLETED (100%)

NAME OF CONTRACTOR:

WODROX LIMITED

DATE OF AWARD:

27-12-2019

CONTRACT SUM:

₦14, 000,000

PROJECT IMPACT ASSESSMENT: CLASS ROOM IN USE



28.03 GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

SOUTH WEST

EKITI

EYIO EKITI

EYIO EKITI VILLAGE

CONSTRUCTION OF A BLOCK OF 2 CLASSROOMS

COMPLETED (100%)

CITI PETROLEUM NIGERIA LIMITED

27-12-2019

N11, 000,000

CLASS ROOM IN USE



28.04 GEO-POLITICAL ZONE:

SOUTH WEST

STATE:

EKITI

LGA:

EYIO EKITI

PROJECT LOCATION:

EYIO EKITI VILLAGE

PROJECT TITLE:

PROVISION OF MOTORIZED BOREHOLE

STATUS OF PROJECT:

COMPLETED (100%)

NAME OF CONTRACTOR:

HENRY ANNE INVESTMENT LTD

DATE OF AWARD:

27-12-2019

CONTRACT SUM:

N11, 000,000.00

PROJECT IMPACT ASSESSMENT: IMPROVE QUALITY OF PORTABLE WATER



28.05 GEO-POLITICAL ZONE:

SOUTH WEST

STATE:

EKITI

LGA:

EYIO EKITI

PROJECT LOCATION:

IDERO EKITI

PROJECT TITLE:

CONSTRUCTION OF A BLOCK OF 3 CLASSROOMS

STATUS OF PROJECT:

COMPLETED (100%)

NAME OF CONTRACTOR:

GIANT MULTI STRIDE ENG LTD

DATE OF AWARD:

27-12-2019

CONTRACT SUM:

N14, 000,000.00

PROJECT IMPACT ASSESSMENT: CLASS ROOMS COMPLETED AND IN USE



29.0

ZONE:

SOUTH WEST

STATE:

ONDO

LGA:

AKURE NORTH

LOCATION:

AKURE

TITLE:

CONSTRUCTION AND RENOVATION OF STRATEGIC ECONOMIC ROADS

STATUS:

COMPLETED AND IN USE

NAME OF CONTRACTOR:

BISHMUR LTD.

DATE OF AWARD:

27/ 12/2019

CONTRACT SUM:

N83,333,333.33

IMPACT ASSESSMENT:

CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADDED VALUE AND BEAUTY TO THE COMMUNITY AND CONTROL FLOOD IN THE ENVIRONMENT, GIVE EASY ACCESS TO THE COMMUNITY.



29.01 ZONE:

STATE:

LGA:

LOCATION:

TITLE:

STATUS:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

IMPACT ASSESSMENT:

SOUTH WEST

ONDO

AKURE SOUTH

AKURE

CONSTRUCTION OF A BLOCK OF 2 CLASSROOMS

COMPLETED AND IN USE

HAJIA RISIKAT BAACRICIZA NIG. LTD

27/ 12/2019

N12,965,400.00

CREATE JOB WITHIN THE COMMUNITY DURING CONSTRUCTION, IT ADD VALUE AND BEAUTY TO THE SCHOOL AND CREATE GOOD AND CONDUCTIVE ENVIRONMENT FOR LEARNING.



29.02 ZONE:

STATE:

LGA:

LOCATION:

TITLE:

STATUS:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

IMPACT ASSESSMENT:

SOUTH WEST

ONDO

OKITIPUPA

METHODIST PRIMARY SCHOOL,

OKITIPUPA

CONSTRUCTION OF A BLOCK OF 2
CLASSROOMS

COMPLETED AND IN USE

COULDRON NIG. LTD.

27/ 12/2019

N12,965,400.00

CREATE JOB WITHIN THE COMMUNITY
DURING CONSTRUCTION, IT ADD VALUE
AND BEAUTY TO THE SCHOOL AND
CREATE GOOD ENVIRONMENT FOR
LEARNING.



30.0 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	RIVERS
LOCAL GOVERNMENT:	AHOADA EAST
PROJECT LOCATION:	OGBOLOMA
PROJECT TITLE:	CONSTRUCTION OF MATERNITY CENTRE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	OZEE ADIBE INTEGRATED LTD.
DATE OF AWARD:	19 - 12 - 2019
CONTRACT SUM:	16,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS NOT BEEN PUT TO USE



30.01 GEOPOLITICAL ZONE:

STATE:

LOCAL GOVERNMENT:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

SOUTH SOUTH

RIVERS

PORTHARCOURT CITY

FEDERAL SECRETARIAT PORTHARCOURT
PROVISION OF INFRASTRUCTURE (SEWAGE)
AT FEDERAL SECRETARIAT PORTHARCOURT,
RIVERS STATE


ON-GOING

ELEKU CONSTRUCTION LTD.


27 - 12 - 2019

16,731,608.57


THE PROJECT IS ON-GOING

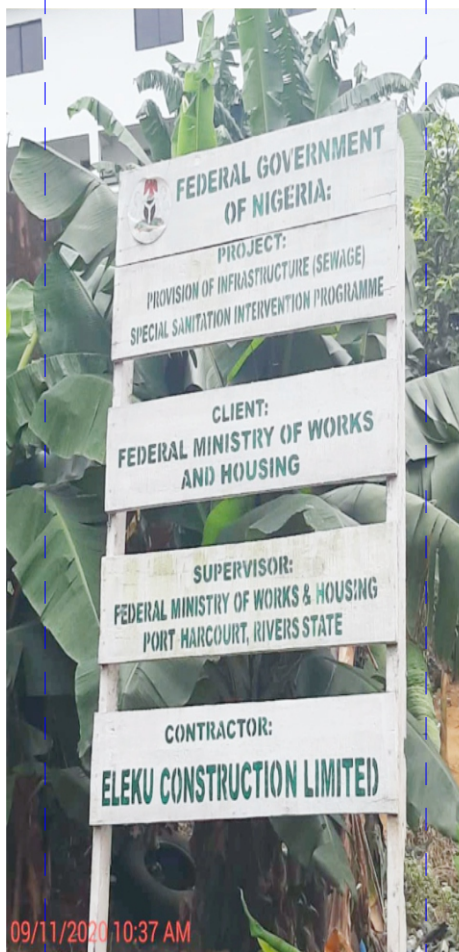

30.02 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	RIVERS
LOCAL GOVERNMENT:	PORTHARCOURT CITY
PROJECT LOCATION:	FEDERAL SECRETARIAT PORTHARCOURT
PROJECT TITLE:	DEBULKING OF FED. SCERETARIAT COMPLEX METERING SYSTEM, PORTHARCOURT, RIVERS STATE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	KUL-DWELL NIG. LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	9,356,025.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS BEEN PUT TO USE

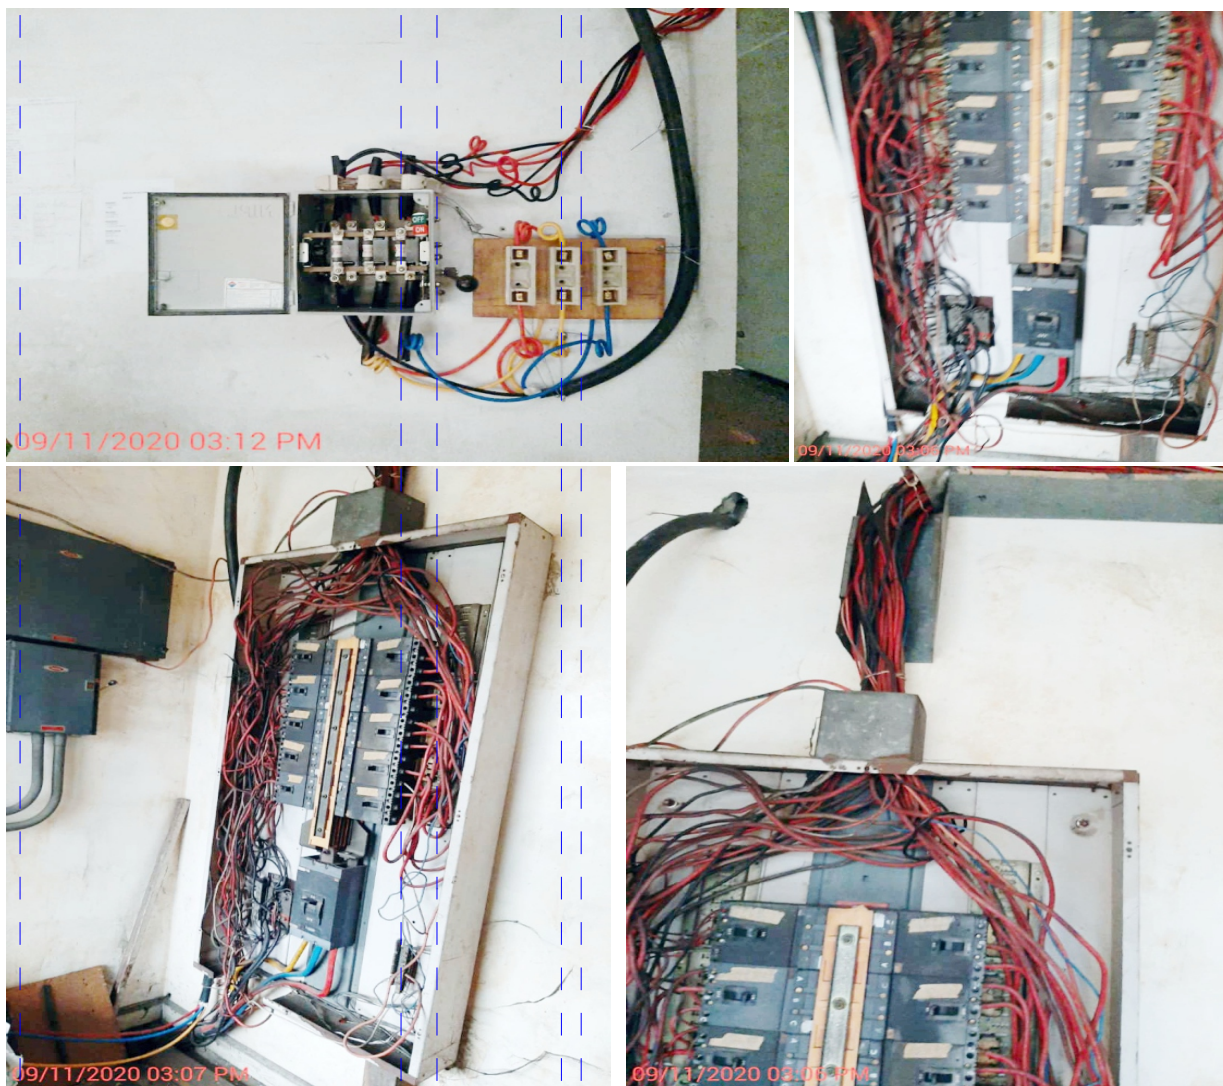

30.03	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	RIVERS
	LOCAL GOVERNMENT:	PORTHARCOURT CITY
	PROJECT LOCATION:	FEDERAL SECRETARIAT PORTHARCOURT
	PROJECT TITLE:	REHABILITATION AND MAINTENANCE OF THE FIRE FIGHTING SYSTEM AT THE FEDERAL SECRETARIAT PORTHARCOURT, RIVERS STATE
	STATUS OF PROJECT:	ON-GOING
	NAME OF CONTRACTOR:	M/S GGB NOYCEE NIG. LTD.
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	24,000,000.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS ON-GOING

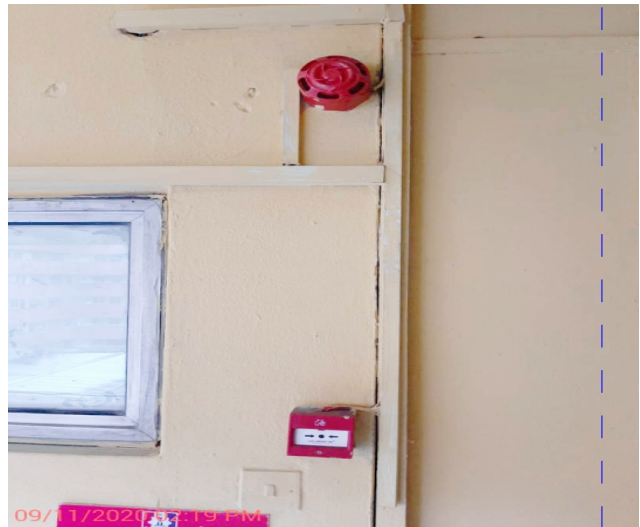

30.04 GEOPOLITICAL ZONE:

STATE:

LOCAL GOVERNMENT:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT: THE PROJECT HAS BEEN PUT TO USE

SOUTH SOUTH

RIVERS

PORTHARCOURT CITY

FEDERAL SECRETARIAT PORTHARCOURT

REHABILITATION AND MAINTENANCE OF

PREVENTION AND FIGHTING SYSTEM

(ELECTRICAL) AT FEDERAL SECRETARIAT




PORTHARCOURT, RIVERS STATE

COMPLETED

SEM-LUK VENTURES LTD.

27 - 12 - 2019

25,500,000.00

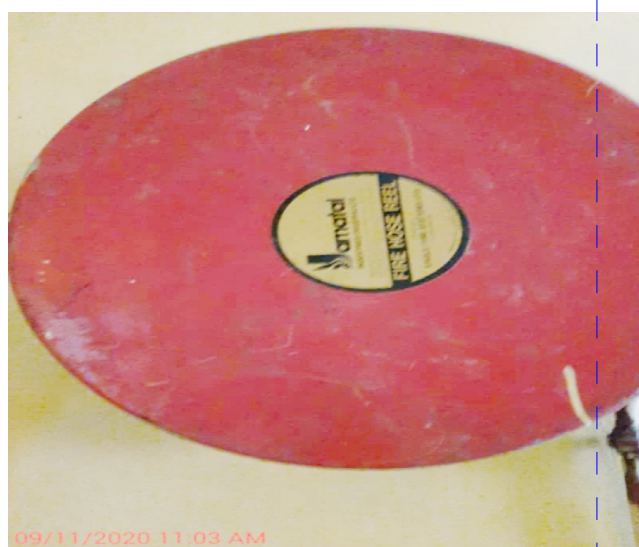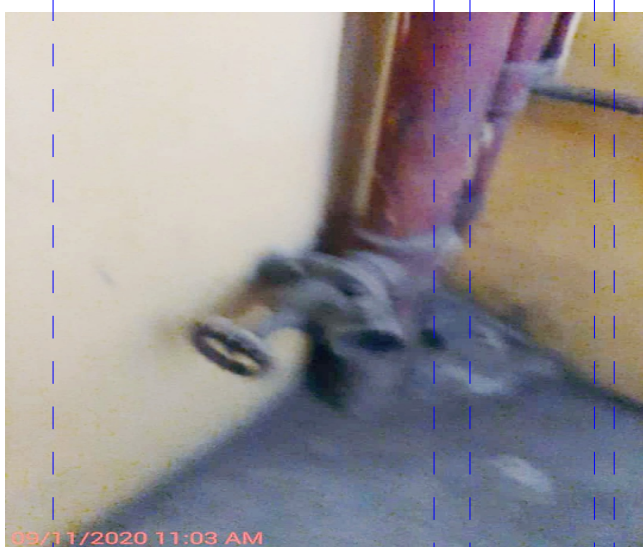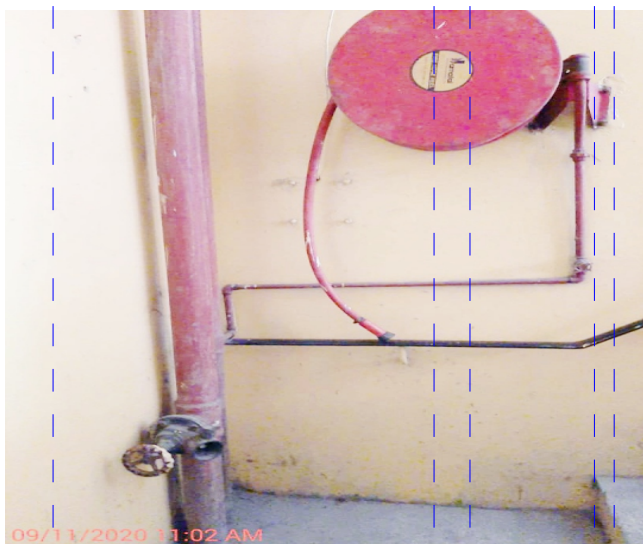

31.0	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	EDO
	LOCAL GOVERNMENT:	ETSAKO WEST LGA
	PROJECT LOCATION:	IYUKU
	PROJECT TITLE:	CONSTRUCTION OF MATERNITY
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	ALOT MULTISYSTEMS LTD.
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	14,065,122.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS NOT BEEN PUT TO USE



31.01 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	EDO
LOCAL GOVERNMENT:	ETSAKO WEST LGA
PROJECT LOCATION:	EGEONO
PROJECT TITLE:	CONSTRUCTION OF MATERNITY
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	NALOT MULTISYSTEMS LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	14,065,122.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS NOT BEEN PUT TO USE



31.02	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	EDO
	LOCAL GOVERNMENT:	AKOKO EDO LGA
	PROJECT LOCATION:	MAKEKE SECONDARY SCHOOL
	PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 2 CLASS ROOM
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	TOMLAD NIGERIA LTD.
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	12,965,400.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS BEEN PUT TO USE



31.03 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	EDO
LOCAL GOVERNMENT:	ETSAKO CENTRAL LGA
PROJECT LOCATION:	MOMOH PRIMARY SCHOOL, VIENAKE, EKPENI
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 6 CLASS ROOM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	TESTED ENGINEERING CONSTRUCTION LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	25,930,800.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS BEEN PUT TO USE



31.04 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	EDO
LOCAL GOVERNMENT:	ETSAKO WEST LGA
PROJECT LOCATION:	AFOWA PRIMARY SCHOOL
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 6 CLASS ROOM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	TESTED ENGINEERING CONSTRUCTION LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	25,930,800.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT HAS BEEN PUT TO USE



32.0

GEO-POLITICAL ZONE:

STATE:

LGA:

PROJECT LOCATION:

PROJECT TITLE:

STATUS OF PROJECT:

NAME OF CONTRACTOR:

DATE OF AWARD:

CONTRACT SUM:

PROJECT IMPACT ASSESMENT:

SOUTH SOUTH

BAYELSA

YENEGOA

YENEGOA BAYELSA STATE, FEDERAL SECRETARIAT.

COMPLETION OF THE CONSTRUCTION OF FEDERAL SECRETARIAT BAYELSA STATE.

ONGOING (85%)

TRENUR NIGERIA LTD.

9-12-2011

N2,563,476,419.85

THE PROJECT IS ON-GOING



33.0	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	CROSS RIVER
	LOCAL GOVERNMENT:	OGOJA LGA
	PROJECT LOCATION:	OGOJA
	PROJECT TITLE:	CONSTRUCTION OF DEEPWELL BOREHOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	JAY JAY BADMUS INVESTMENT LTD.
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	83,350,000.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



33.01 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	CROSS RIVER
LOCAL GOVERNMENT:	OBUDU LGA
PROJECT LOCATION:	OBUDU KINGDOM
PROJECT TITLE:	SUPPLY INSTALLATION OF 500KVA TRANSFORMER
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	BABANGIDA STANDARD CONTRACTORS LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	13,000,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING




33.02 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	CROSS RIVER
LOCAL GOVERNMENT:	YALA LGA
PROJECT LOCATION:	YALA
PROJECT TITLE:	CONSTRUCTION OF DEEPWELL BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	JAY JAY BADMUS INVESTMENT LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	83,350,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



33.03 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	CROSS RIVER
LOCAL GOVERNMENT:	OBALIKU/OBUDU/BEKWARRA LGA
PROJECT LOCATION:	OBUDU
PROJECT TITLE:	CONSTRUCTION OF A BLOCK OF 3 CLASS ROOM
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	SHENZOVIC & ZEMDI LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	23,300,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



33.04 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	CROSS RIVER
LOCAL GOVERNMENT:	OGOJA LGA
PROJECT LOCATION:	ESHINJOK-NWANG ROAD
PROJECT TITLE:	CONSTRUCTION OF ROAD, DRAINAGE AND BRIDGE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	BLACK GOLD CONSTRUCTION LTD.
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	149,321,002.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING

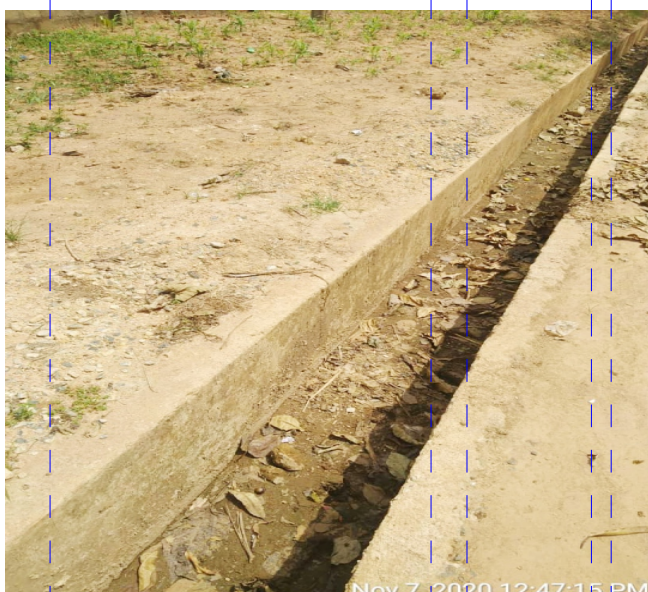

34.0	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	DELTA
	LOCAL GOVERNMENT:	OSHIMILI NORTH
	PROJECT LOCATION:	FEDERAL SECRETARIAT ASABA
	PROJECT TITLE:	PROVISION OF MOTORISED BOREHOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	SAINT AIMS INTERNATIONAL LTD.
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	10,187,100.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS NOT FULLY UTILIZED



34.01 GEOPOLITICAL ZONE:

SOUTH SOUTH

STATE:

DELTA

LOCAL GOVERNMENT:

ANIOCHA NORTH

PROJECT LOCATION:

ONICHA UGBO

PROJECT TITLE:

PROVISION AND INSTALLATION 10 POLES
OF ALL IN ONE SOLAR STREET LIGHT

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

AJ & C INTEGRATED LTD.

DATE OF AWARD:

27 - 12 - 2019

CONTRACT SUM:

9,250,000.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



34.02 GEOPOLITICAL ZONE:	SOUTH SOUTH
STATE:	DELTA
LOCAL GOVERNMENT:	IKA SOUTH LGA
PROJECT LOCATION:	ABAVO
PROJECT TITLE:	CONSTRUCTION OF 5 NO. DEEPWELL BOREHOLE
STATUS OF PROJECT:	COMPLETED
NAME OF CONTRACTOR:	MONNEX GLOBAL RESOURCES LIMITED
DATE OF AWARD:	27 - 12 - 2019
CONTRACT SUM:	82,930,000.00
PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



34.03	GEOPOLITICAL ZONE:	SOUTH SOUTH
	STATE:	DELTA
	LOCAL GOVERNMENT:	ISOKO NORTH
	PROJECT LOCATION:	OZORO
	PROJECT TITLE:	CONSTRUCTION OF 5 NO. DEEPWELL BOREHOLE
	STATUS OF PROJECT:	COMPLETED
	NAME OF CONTRACTOR:	MONNEX GLOBAL RESOURCES LIMITED
	DATE OF AWARD:	27 - 12 - 2019
	CONTRACT SUM:	82,930,000.00
	PROJECT IMPACT ASSESSMENT:	THE PROJECT IS FUNCTIONING



34.04 GEOPOLITICAL ZONE:

SOUTH SOUTH

STATE:

DELTA

LOCAL GOVERNMENT:

ISOKO NORTH

PROJECT LOCATION:

ELLU ISOKO NORTH LGA

PROJECT TITLE:

PROVISION OF SOLAR POWERED BOREHOLE

STATUS OF PROJECT:

COMPLETED

NAME OF CONTRACTOR:

DEREKSON LTD.

DATE OF AWARD:

27 - 12 - 2019

CONTRACT SUM:

11,666,666.00

PROJECT IMPACT ASSESSMENT:

THE PROJECT IS FUNCTIONING



35.0

GEO-POLITICAL ZONE:

STATE:

PROJECT TITLE:

PROJECT LOCATION:

NAME OF CONTRACTOR:

DATE OF AWARD:

LGA:

STATUS OF PROJECT:

CONTRACT SUM:

PROJECT IMPACT ASSESSMENT:

SOUTH-SOUTH

AKWA IBOM

PROVISION OF SOLAR POWERED
BOREHOLE

AKPAN AFIA STREET, MBIOKPORO 1 NSIT
IBOM LGA

FOGA ASSOCIATE LIMITED


27TH DECEMBER, 2019

IBESIKPO ASUTAW

COMPLETED

N11,666,666.00

PROVIDE LIGHT/ELECTICITY FOR THE
COMMUNITY ENHANCE BUSINESS
OPPORTUNITY.

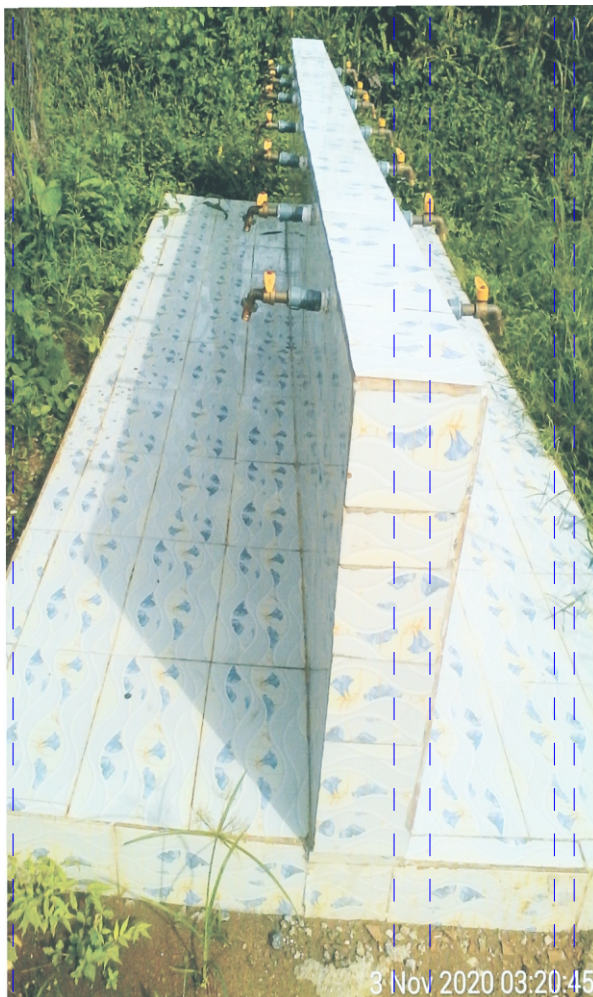

35.01 GEO-POLITICAL ZONE: SOUTH-SOUTH

STATE: AKWA IBOM

PROJECT TITLE: PROVISION AND INSTALLATION 10POLES OF ALL IN ONE SOLAR STREET LIGHTING IN AKWA IBOM

PROJECT LOCATION: IBESIKPO ASUTAN AFAHA ETOK BY CHIEF HILARY HOUSE AFAHA ETOK BY UDOBIA STREET, AFAHA ETOK BY CIVIL CENTER AFAHA ETOK BY APOSTOLIC CHURCH ETC. (ALL PROJECTS LOCATED IN THAT IBESIKPO ASUTAN LGA)

NAME OF CONTRACTOR: DIGMA INTEGRATED SERVICE LIMITED

DATE OF AWARD: 27TH DECEMBER, 2019

LGA: IBESIKPO ASUTAN

STATUS OF PROJECT: COMPLETED

CONTRACT SUM: N9,250,000.00

PROJECT IMPACT ASSESSMENT: PROVIDE LIGHT/ELECTICITY TO THE COMMUNITY TO ENHANCE BUSINESS OPPORTUNITY.



3 Nov 2020 03:50:05



3 Nov 2020 03:51:17




3 Nov 2020 03:51:45



3 Nov 2020 04:01:06



3 Nov 2020 04:06:22

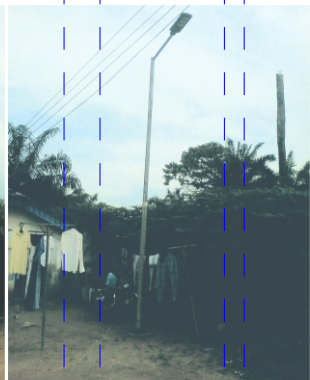

3 Nov 2020 04:09:19



3 Nov 2020 03:51:37



3 Nov 2020 04:01:06

1 NO. SOLAR STREET LIGHT AT AFAHA ETOK IBESIKPO ASUTAN LGA BY UDOBIA STREET

1 NO. SOLAR STREET LIGHT AT AFAHA ETOK IBESIKPO ASUTAN LGA

1 NO. SOLAR STREET LIGHT AT AFAHA ETOK IBESIKPO ASUTAN LGA

1 NO. SOLAR STREET LIGHT AT AFAHA ETOK IBESIKPO ASUTAN LGA BY AFAHA ROAD

35.02 GEO-POLITICAL ZONE:
STATE:
PROJECT TITLE:

SOUTH-SOUTH
AKWA IBOM
PROVISION AND INSTALLATION 10POLES OF
ALL IN ONE SOLAR STREET LIGHTING IN
AKWA IBOM

PROJECT LOCATION:

IBESEKPO ASUTAN AFAHA ETOK BY CHIEF HILARY HOUSE AFAHA ETOK BY UDOBIA STREET, AFAHA ETOK BY CIVIL CENTER AFAHA ETOK BY APOSTOLIC CHURCH ETC. (ALL PROJECTS LOCATED IN THAT IBESIKPO ASUTAN LGA)

NAME OF CONTRACTOR:

DIGMA INTEGRATED SERVICE LIMITED

DATE OF AWARD:

27TH DECEMBER, 2019

LGA:

IBESIKPO ASUTAN

STATUS OF PROJECT:

COMPLETED

CONTRACT SUM:

N9,250,000.00

PROJECT IMPACT

ASSESSMENT:

PROVIDE LIGHT/ELECTICITY TO THE COMMUNITY TO ENHANCE BUSINESS OPPORTUNITY.



3 Nov 2020 04:14:39



Oct 30, 2020 2:35:48 PM
Akure Ilesha Road
Akure North
Ondo



4 Nov 2020 15:04:33
Unnamed Road
Potiskum
Yobe



4 Nov 2020 15:03:21
Unnamed Road
Potiskum
Yobe
